Osoyoos

Canada's warmest welcome

WATER

Annual Report 2011

2011

Submitted by:

Osoyoos

Canada's warmest welcome

Town of Osoyoos
8707 Main Street
Box 3010
Osoyoos, BC V0H 1V0

Prepared by:

Ron Doucette
Director of Operational Services

February, 2012

Town of Osoyoos
Water Annual Repor

Water

Annual Report 2011

Submitted by:

Town of Osoyoos
8707 Main Street
Box 3010
Osoyoos, BC V0H 1V0

Prepared by:

Ron Doucette
Director of Operational Services

Table of Contents

System Description 1
Operator Certification 1
Bacteriological Summary 1
Capital Works Plan 2
Water Monitoring Plan 2
Water System Assessment 3
Water Master Plan 3
Water Consumption Summary 4
Well Monthly Summary 6
Monthly Chlorine Consumption 8
Charts 9
Chemical Analysis 10
Cross Connection Program 17

System Description

The Town of Osoyoos has a Class II Water Distribution System. The source of water comes from five different wells with three reservoirs. The water is untreated with one well equipped with a standby chlorinator if necessary. A cross connection program is in effect. Attached to the report is a copy of the up to date cross connection program that includes new services and existing facility survey status.

Operator Certification

The Town of Osoyoos has **five certified** operators:

Karl Fichter	Certificate #6840
Leigh Lougheed	Certificate #6846
David Stene	Certificate #6851
Mike Thomas	Certificate #3219
Frank Zandvliet	Certificate #5657

The Town of Osoyoos also has an Irrigation System with two lake inlets and one well that provide domestic water in the non-irrigation season; all irrigation water sources are treated. Chlorinator residual testing is done daily during the irrigation season and well testing during the non-irrigation season is done a minimum of twice a week.

Bacteriological Summary

The Town of Osoyoos collected 106 Coliform Samples for the Irrigation system.

The Town of Osoyoos collected 49 Coliform Samples for the Town System.

The Irrigation system also had Trihalomethane analysis done. Results are enclosed in the following reports from Caro. Attached for your perusal is various water reports taken for the Town of Osoyoos Water System.

Capital Works Plan

The following is an update for 2011 Capital Projects:

- Water Meters install on high end user including Park Irrigation
- GUDI Report soon to be complete
- 340 Reservoir schedule completion in spring of 2012
- Pumphouse #9 for the SO Irrigation District electrical upgrades scheduled completion for Spring of 2012
- Water Distribution Upgrades 74th to Curlew completed

The 2012 **proposed** Capital Projects for the Town of Osoyoos Water System include the following:

- Pilot test for Manganese Removal
- Improvements to the SCADA system

Water Monitoring Plan

The following is the Water Monitoring Schedule for the Town of Osoyoos Water System and the Town of Osoyoos System 8 & 9 Irrigation systems:

January 1 to Dec 31, 2012	Weekly Sampling for Bacterial Coliform and E-Coli
June 12, 2012	Nitrate/Nitrite/Hardness/Manganese
August 7, 2012	THM's System #8 & #9
September 11, 2012	Chemical and Bacterial Parameters for Well #8
September 12, 2012	Nitrate/Nitrite/Hardness/Manganese
December 4, 2012	THM's System #8 & #9
December 11, 2012	Nitrate/Nitrite/Hardness/Manganese

We will be doing weekly samples of the Beaches as outlined by Interior Health from July 3rd to September 4, 2012.

Water System Assessment

The Town of Osoyoos hired Western Water Associates Ltd. to undertake a GWUDI assessment of the Town's six municipal system water supply wells. The Town of Osoyoos submitted Phase 1 of the report to Interior Health in March of 2011 and followed up with a meeting in May of 2011.

The Town discussed with Interior Health Officials the scope of the work for Phase 2 assessment and the program. Western Water began the assessment in the summer and early fall of 2011. The GWUDI assessment final report is anticipated to be submitted to Interior Health in the spring of 2012.

The Town of Osoyoos applied for a capital grant for Phase 1 of the Twinning Program (south half of irrigation System #8) was made under Gas Tax Agreement's General Strategic Priorities Fund (GSPF) in April 2011. In January of 2012, the Town was advised that the application was not approved.

Water Master Plan

To date the Water Master Plan relating to Irrigation District Systems 8 & 9 has been completed and adopted by the Town. The master plan for the Irrigation systems recommends a twinning program 43210 compliance.

The master plan for the municipal water system has not been completed because of uncertainties related to GWUDI classification of the Town water supply wells. It is anticipated that finalization of the GWUDI assessment report by Western Water will provide the basis for developing 43210 compliance plans for each well and thereby enable completion of components of the water master plan which relate to the municipal water system.

Water Consumption Summary

Water Consumption - Town System

Well #	2011	2010	2009
1	251,949 m^3	199,300 m^3	
3	1,004,705 m^3	961,295 m^3	399,375 m^3
4	134,513 m^3	79,312 m^3	613,735 m^3
5	368,432 m^3	311,375 m^3	666,174 m^3
6	66,902 m^3	118,968 m^3	140,065 m^3
8	332,527 m^3	436,625 m^3	601,205 m^3
Total	2,159,028 m^3	2,106,875 m^3	2,502,300 m^3

Water Consumption - Irrigation System

	2011	2010	2009
System 8	4,097,360 m^3	3,719,939m^3	4,356,220 m^3
System 9	3,069,815 m^3	4,253,358m^3	3,102,082 m^3
Well #6	220,166 m^3	253,193m^3	254,054 m^3
Total	7,387,341 m^3	7,238,419 m^3	7,712,356 m^3

Total Chlorine Used = 14530.8 kg

Well #6 - Water Consumption 2011

Month	Hrs Ran	In Min	x gpm	m^3
January	386	23,160	516	45,283
February	337	20,220	518	39,689
March	349	20,940	517	40,983
April	236	14,160	514	27,560
May				
June				
July	165	9,900	501	18,792
August	220	13,200	505	25,230
September	84	5040	501	9558
October	117	7,020	501	13,322
November	309	18,540	511	35,861
December	262	15,720	517	30,790
Total	**2,465**	**147,900**	**510**	**287,068 m^3**
To Town Water System July, Aug, Sept and Oct =				66,902 m^3
To Irrigation System All Other Months =				220,166 m^3

System 8
Water Consumption 2011

Month	m^3
January	77,148
February	2,038
March	2,193
April	111,254
May	255,246
June	662
July	534
August	973,648
September	1,127,091
October	752,186
November	130,538
December	3,485
Total	**3,436,023 m^3**

System 9
Water Consumption 2011

Month	m^3
January	-
February	-
March	-
April	76,653
May	207,365
June	537,634
July	764,455
August	911,945
September	555,323
October	88,761
November	-
December	-
Total	**3,142,136 m^3**

Well Monthly Summary

Water Well #1
Consumption 2011

Month	m^3	Hrs Ran
January	3,421	48
February	2,058	25
March	3,194	44
April	14,001	198
May	42,134	595
June	44,684	655
July	44,450	745
August	43,708	738
September	38,640	652
October	13,341	221
November	2,319	39
December		
Total	**251,950 m^3**	**3,960**

Water Well #3
Consumption 2011

Month	m^3	Hrs Ran
January	77,614	547
February	58,697	414
March	67,492	476
April	85,845	607
May	101,731	743
June	101,773	719
July	104,886	744
August	104,341	716
September	102,087	721
October	90,098	636
November	55,462	391
December	54,678	385
Total	**1,004,705 m^3**	**7,099**

Water Well #4
Consumption 2011

Month	m^3	Hrs Ran
January	-	-
February	-	-
March	-	-
April	72	1
May	985	5
June	11824	61
July	43,258	218
August	50,978	262
September	27,383	138
October	-	-
November	13	-
December	-	-
Total	**134,513 m^3**	**685**

Water Well #5
Consumption 2011

Month	m^3	Hrs Ran
January	-	-
February	-	-
March	-	-
April	4,674	23
May	36,470	179
June	114,633	217
July	76,155	371
August	84,973	419
September	49,633	242
October	1,883	14
November	11	-
December	-	-
Total	**311,375 m^3**	**1,475**

Well #8 Water Consumption 2011

Month	m^3	Hrs Ran
January	-	-
February	-	-
March	-	-
April	-	-
May	-	-
June	51,129	317
July	99,133	629
August	101,712	660
September	67,193	442
October	12,231	80
November	277	2
December	852	6
Total	**332,527 m^3**	**2,136**

Oscyoos

Monthly Chlorine Consumption

Station 8
Chlorine Consumption

Month	kg
January	-
February	-
March	-
April	204.5
May	509.1
June	1350
July	2040.9
August	2095.5
September	1354.5
October	340.9
November	4.5
December	-
Total	**7900.0 kg**

Station 9
Chlorine Consumption

Month	kg
January	-
February	-
March	-
April	140.9
May	413.6
June	1095.5
July	1604.5
August	1695.5
September	1000
October	231.8
November	-
December	-
Total	**6181.8 kg**

Water Well #6
Chlorine Consumption

Month	**kg**
January	93.6
February	86.4
March	86.8
April	54.5
May	-
June	-
July	14.5
August	19.5
September	8.6
October	27.7
November	70
December	57.7
Total	**519.5 kg**

Charts

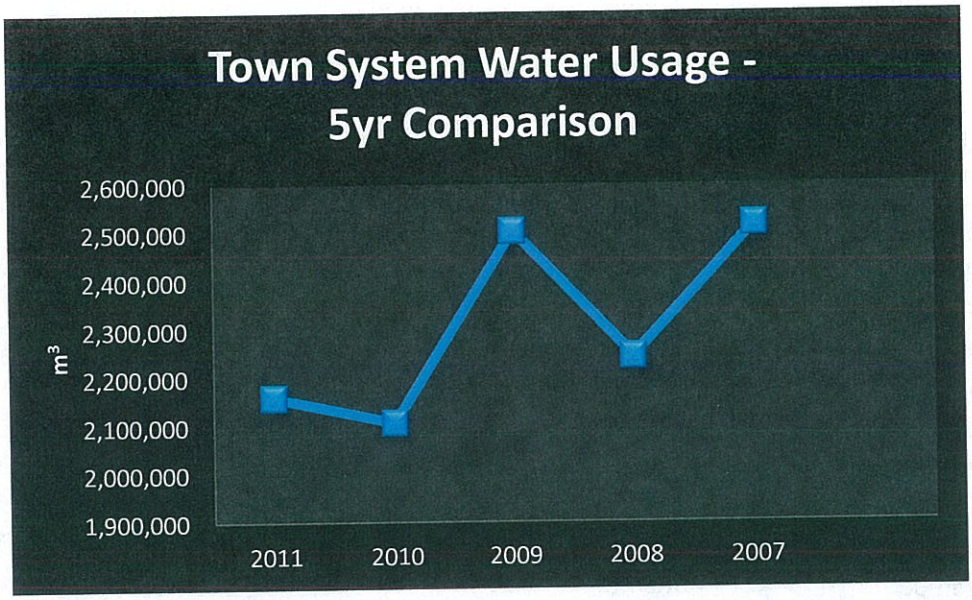
Town System Water Usage -
5yr Comparison
2,600,000
2,500,000
2,400,000
2,300,000
2,200,000
2,100,000
2,000,000
1,900,000
m3
2011
2010
2009
2008
2007

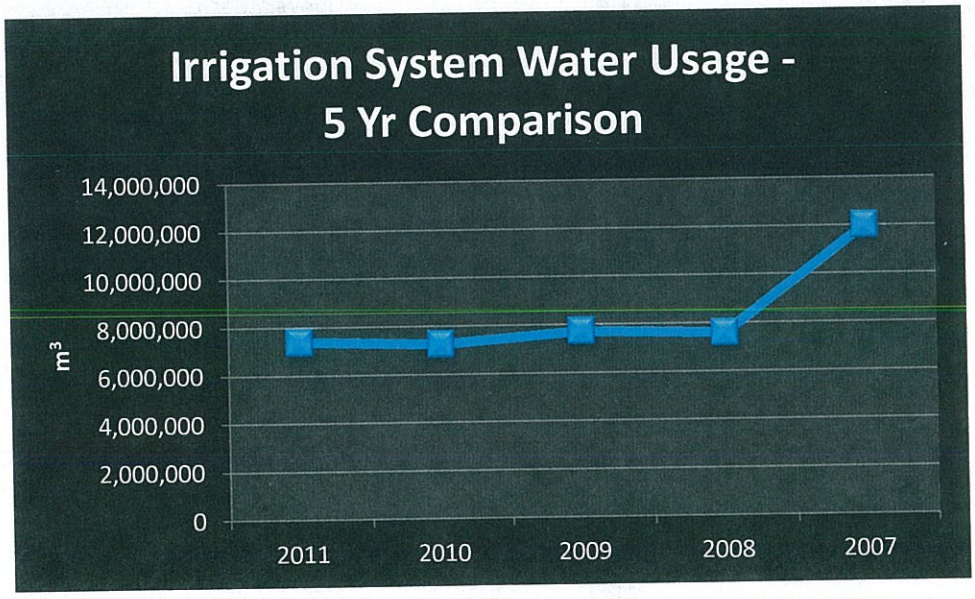
Irrigation System Water Usage -
5 Yr Comparison
14,000,000
12,000,000
10,000,000
8,000,000
6,000,000
4,000,000
2,000,000
0
m3
2011
2010
2009
2008
2007

SAMPLE DATA

CARO ANALYTICAL SERVICES

CLIENT	Osoyoos, Town of	**WORK ORDER #**	K1I0506
PROJECT	Comprehensive Analysis	**REPORTED**	Sep-21-11

Analyte	Result	Canadian DW Guideline (Dec 10)	RDL	Units	Prepared	Analyzed	Notes
General Parameters							
Town Water - Well #5 (K1I0506-01) Matrix: Water Sampled: Sep-13-11 07:30							
Alkalinity, Total as CaCO3	**223**		1.0	mg/L	Sep-15-11	Sep-15-11	
Chloride	**8.58**	AO ≤ 250	0.10	mg/L	Sep-15-11	Sep-15-11	
Colour, True	< 5	AO ≤ 15	5	Color Unit	Sep-15-11	Sep-15-11	
Conductivity (EC)	**453**		2	uS/cm	Sep-15-11	Sep-15-11	
Cyanide (total)	< 0.01	MAC = 0.2	0.01	mg/L	Sep-14-11	Sep-19-11	
Fluoride	**0.48**	MAC = 1.5	0.10	mg/L	Sep-15-11	Sep-15-11	
Hardness, Total (Total as CaCO3)	**216**		5.41	mg/L	Sep-15-11	Sep-19-11	
Nitrogen, Nitrate as N	**0.013**	MAC = 10	0.010	mg/L	Sep-15-11	Sep-15-11	
Nitrogen, Nitrite as N	< 0.01	MAC = 1	0.01	mg/L	Sep-15-11	Sep-15-11	
pH	**8.01**	AO = 6.5 - 8.5	0.01	pH Units	Sep-15-11	Sep-15-11	
Solids, Total Dissolved	**287**	AO ≤ 500	5	mg/L	Sep-20-11	Sep-20-11	
Sulfate	**39.0**	AO ≤ 500	1.0	mg/L	Sep-15-11	Sep-15-11	
Turbidity	**0.29**	Varies, See Guidelines	0.10	NTU	Sep-15-11	Sep-15-11	
UV Transmittance @ 254nm	**88.5**		0.1	%	Sep-16-11	Sep-16-11	
Total Recoverable Metals by ICPMS							
Town Water - Well #5 (K1I0506-01) Matrix: Water Sampled: Sep-13-11 07:30							
Aluminum	< 0.050	AO ≤ 0.1	0.050	mg/L	Sep-15-11	Sep-19-11	
Antimony	< 0.0010	MAC = 0.006	0.0010	mg/L	Sep-15-11	Sep-19-11	
Arsenic	< 0.0050	MAC = 0.01	0.0050	mg/L	Sep-15-11	Sep-19-11	
Barium	**0.104**	MAC = 1	0.050	mg/L	Sep-15-11	Sep-19-11	
Beryllium	< 0.0010		0.0010	mg/L	Sep-15-11	Sep-19-11	
Boron	**0.045**	MAC = 5	0.040	mg/L	Sep-15-11	Sep-19-11	
Cadmium	< 0.00010	MAC = 0.005	0.00010	mg/L	Sep-15-11	Sep-19-11	
Calcium	**51.7**		2.0	mg/L	Sep-15-11	Sep-19-11	
Chromium	< 0.0050	MAC = 0.05	0.0050	mg/L	Sep-15-11	Sep-19-11	
Cobalt	< 0.00050		0.00050	mg/L	Sep-15-11	Sep-19-11	
Copper	**0.0037**	AO ≤ 1	0.0020	mg/L	Sep-15-11	Sep-19-11	
Iron	**0.14**	AO ≤ 0.3	0.10	mg/L	Sep-15-11	Sep-19-11	
Lead	**0.0021**	MAC = 0.01	0.0010	mg/L	Sep-15-11	Sep-19-11	
Magnesium	**21.0**		0.10	mg/L	Sep-15-11	Sep-19-11	
Manganese	**0.126**	AO ≤ 0.05	0.0020	mg/L	Sep-15-11	Sep-19-11	
Mercury	< 0.00020	MAC = 0.001	0.00020	mg/L	Sep-15-11	Sep-19-11	
Molybdenum	**0.0069**		0.0010	mg/L	Sep-15-11	Sep-19-11	
Nickel	< 0.0020		0.0020	mg/L	Sep-15-11	Sep-19-11	
Phosphorus	< 0.20		0.20	mg/L	Sep-15-11	Sep-19-11	
Potassium	**5.07**		0.20	mg/L	Sep-15-11	Sep-19-11	
Selenium	< 0.0050	MAC = 0.01	0.0050	mg/L	Sep-15-11	Sep-19-11	
Silicon	**7.3**		5.0	mg/L	Sep-15-11	Sep-19-11	
Silver	< 0.00050		0.00050	mg/L	Sep-15-11	Sep-19-11	
Sodium	**27.2**	AO ≤ 200	0.20	mg/L	Sep-15-11	Sep-19-11	
Uranium	**0.00621**	MAC = 0.02	0.00020	mg/L	Sep-15-11	Sep-19-11	
Vanadium	< 0.010		0.010	mg/L	Sep-15-11	Sep-19-11	
Zinc	< 0.040	AO ≤ 5	0.040	mg/L	Sep-15-11	Sep-19-11	

SAMPLE DATA

CARO ANALYTICAL SERVICES

CLIENT	Osoyoos, Town of	**WORK ORDER #**	K1I0506
PROJECT	Comprehensive Analysis	**REPORTED**	Sep-21-11

Analyte	Result	Canadian DW Guideline (Dec 10)	RDL	Units	Prepared	Analyzed	Notes
Microbiological Parameters							
Town Water - Well #5 (K1I0506-01) Matrix: Water Sampled: Sep-13-11 07:30							
Coliforms, Total	< 1	MAC < 1	1	CFU/100mL	Sep-14-11	Sep-15-11	
E. coli	< 1	MAC < 1	1	CFU/100mL	Sep-14-11	Sep-15-11	

SAMPLE DATA

CARO ANALYTICAL SERVICES

CLIENT	Osoyoos, Town of	**WORK ORDER #**	K1H0393
PROJECT	Drinking Water	**REPORTED**	Aug-16-11

Analyte	Result	Canadian DW Guideline (Dec 10)	RDL	Units	Prepared	Analyzed	Notes
Volatile Organic Compounds by GCMS							
System #9, 10021 42nd Street (K1H0393-01) Matrix: Water Sampled: Aug-09-11 08:45							
Bromodichloromethane	**0.002**		0.001	mg/L	Aug-11-11	Aug-12-11	
Bromoform	< 0.001		0.001	mg/L	Aug-11-11	Aug-12-11	
Chloroform	**0.043**		0.001	mg/L	Aug-11-11	Aug-12-11	
Dibromochloromethane	< 0.001		0.001	mg/L	Aug-11-11	Aug-12-11	
Trihalomethanes (total)	**0.045**	MAC = 0.1	0.004	mg/L	Aug-11-11	Aug-12-11	
Surrogate: 4-Bromofluorobenzene	*103 %*		*80-120*		*Aug-11-11*	*Aug-12-11*	

SAMPLE DATA

CARO ANALYTICAL SERVICES

CLIENT	Osoyoos, Town of	**WORK ORDER #**	K1H0385
PROJECT	THM Analysis	**REPORTED**	Aug-16-11

Analyte	Result	Canadian DW Guideline (Dec 10)	RDL	Units	Prepared	Analyzed	Notes
Volatile Organic Compounds by GCMS							
System #8 9707 87th Street (K1H0385-01) Matrix: Water Sampled: Aug-09-11 08:45							
Bromodichloromethane	**0.002**		0.001	mg/L	Aug-11-11	Aug-12-11	
Bromoform	< 0.001		0.001	mg/L	Aug-11-11	Aug-12-11	
Chloroform	**0.049**		0.001	mg/L	Aug-11-11	Aug-12-11	
Dibromochloromethane	< 0.001		0.001	mg/L	Aug-11-11	Aug-12-11	
Trihalomethanes (total)	**0.051**	MAC = 0.1	0.004	mg/L	Aug-11-11	Aug-12-11	
Surrogate: 4-Bromofluorobenzene	*110 %*		*80-120*		*Aug-11-11*	*Aug-12-11*	

SAMPLE DATA

CARO ANALYTICAL SERVICES

CLIENT	Osoyoos, Town of	**WORK ORDER #**	K1H0393
PROJECT	Drinking Water	**REPORTED**	Aug-16-11

Analyte	Result	Canadian DW Guideline (Dec 10)	RDL	Units	Prepared	Analyzed	Notes
Volatile Organic Compounds by GCMS							
System #9, 10021 42nd Street (K1H0393-01) Matrix: Water Sampled: Aug-09-11 08:45							
Bromodichloromethane	**0.002**		0.001	mg/L	Aug-11-11	Aug-12-11	
Bromoform	< 0.001		0.001	mg/L	Aug-11-11	Aug-12-11	
Chloroform	**0.043**		0.001	mg/L	Aug-11-11	Aug-12-11	
Dibromochloromethane	< 0.001		0.001	mg/L	Aug-11-11	Aug-12-11	
Trihalomethanes (total)	**0.045**	MAC = 0.1	0.004	mg/L	Aug-11-11	Aug-12-11	
Surrogate: 4-Bromofluorobenzene	*103 %*		*80-120*		*Aug-11-11*	*Aug-12-11*	

SAMPLE DATA

CARO ANALYTICAL SERVICES

CLIENT	Osoyoos, Town of	**WORK ORDER #**	K1H0385
PROJECT	THM Analysis	**REPORTED**	Aug-16-11

Analyte	Result	Canadian DW Guideline (Dec 10)	RDL	Units	Prepared	Analyzed	Notes
Volatile Organic Compounds by GCMS							
System #8 9707 87th Street (K1H0385-01) Matrix: Water Sampled: Aug-09-11 08:45							
Bromodichloromethane	**0.002**		0.001	mg/L	Aug-11-11	Aug-12-11	
Bromoform	< 0.001		0.001	mg/L	Aug-11-11	Aug-12-11	
Chloroform	**0.049**		0.001	mg/L	Aug-11-11	Aug-12-11	
Dibromochloromethane	< 0.001		0.001	mg/L	Aug-11-11	Aug-12-11	
Trihalomethanes (total)	**0.051**	MAC = 0.1	0.004	mg/L	Aug-11-11	Aug-12-11	
Surrogate: 4-Bromofluorobenzene	*110 %*		*80-120*		*Aug-11-11*	*Aug-12-11*	

SAMPLE DATA

CARO ANALYTICAL SERVICES

CLIENT	Osoyoos, Town of	**WORK ORDER #**	K1L0239
PROJECT	Drinking Water	**REPORTED**	Dec-19-11

Volatile Organic Compounds

Analyte	Result	Canadian DW Guideline (Dec 10)	RDL	Units	Prepared	Analyzed	Notes
System #8 - 9103-100th (K1L0239-01) Matrix: Water Sampled: Dec-06-11 10:30							
Bromodichloromethane	**0.002**		0.001	mg/L	Dec-15-11	Dec-16-11	
Bromoform	< 0.001		0.001	mg/L	Dec-15-11	Dec-16-11	
Chloroform	**0.005**		0.001	mg/L	Dec-15-11	Dec-16-11	
Dibromochloromethane	< 0.001		0.001	mg/L	Dec-15-11	Dec-16-11	
Trihalomethanes (total)	**0.008**	MAC = 0.1	0.004	mg/L	Dec-15-11	Dec-16-11	
Surrogate: 4-Bromofluorobenzene	*105 %*		*80-120*		*Dec-15-11*	*Dec-16-11*	

SAMPLE DATA

CARO ANALYTICAL SERVICES

CLIENT	Osoyoos, Town of	**WORK ORDER #**	K1L0240
PROJECT	Drinking Water	**REPORTED**	Dec-19-11

Analyte	Result	Canadian DW Guideline (Dec 10)	RDL	Units	Prepared	Analyzed	Notes
Volatile Organic Compounds							
System #9, 10021 42nd Ave (K1L0240-01) Matrix: Water Sampled: Dec-06-11 10:45							
Bromodichloromethane	**0.002**		0.001	mg/L	Dec-15-11	Dec-16-11	
Bromoform	< 0.001		0.001	mg/L	Dec-15-11	Dec-16-11	
Chloroform	**0.006**		0.001	mg/L	Dec-15-11	Dec-16-11	
Dibromochloromethane	< 0.001		0.001	mg/L	Dec-15-11	Dec-16-11	
Trihalomethanes (total)	**0.009**	MAC = 0.1	0.004	mg/L	Dec-15-11	Dec-16-11	
Surrogate: 4-Bromofluorobenzene	*102 %*		*80-120*		*Dec-15-11*	*Dec-16-11*	

Cross Connection Program

The Town of Osoyoos currently has a Cross Connection program in place.

See the following pages for various reports that contain information on the Town's Cross Connection program.

Cross-Connection Control Program Summary Report
[February 01, 2012]

Customers	**335**
BFP's Tracked	**237**

Hazards	Quantity	Not Surveyed	Surveyed	Vacant	Compliant
High	94	5	89	0	57
Medium	111	73	37	1	27
Low	56	17	39	0	12
Total	261	95	165	1	96

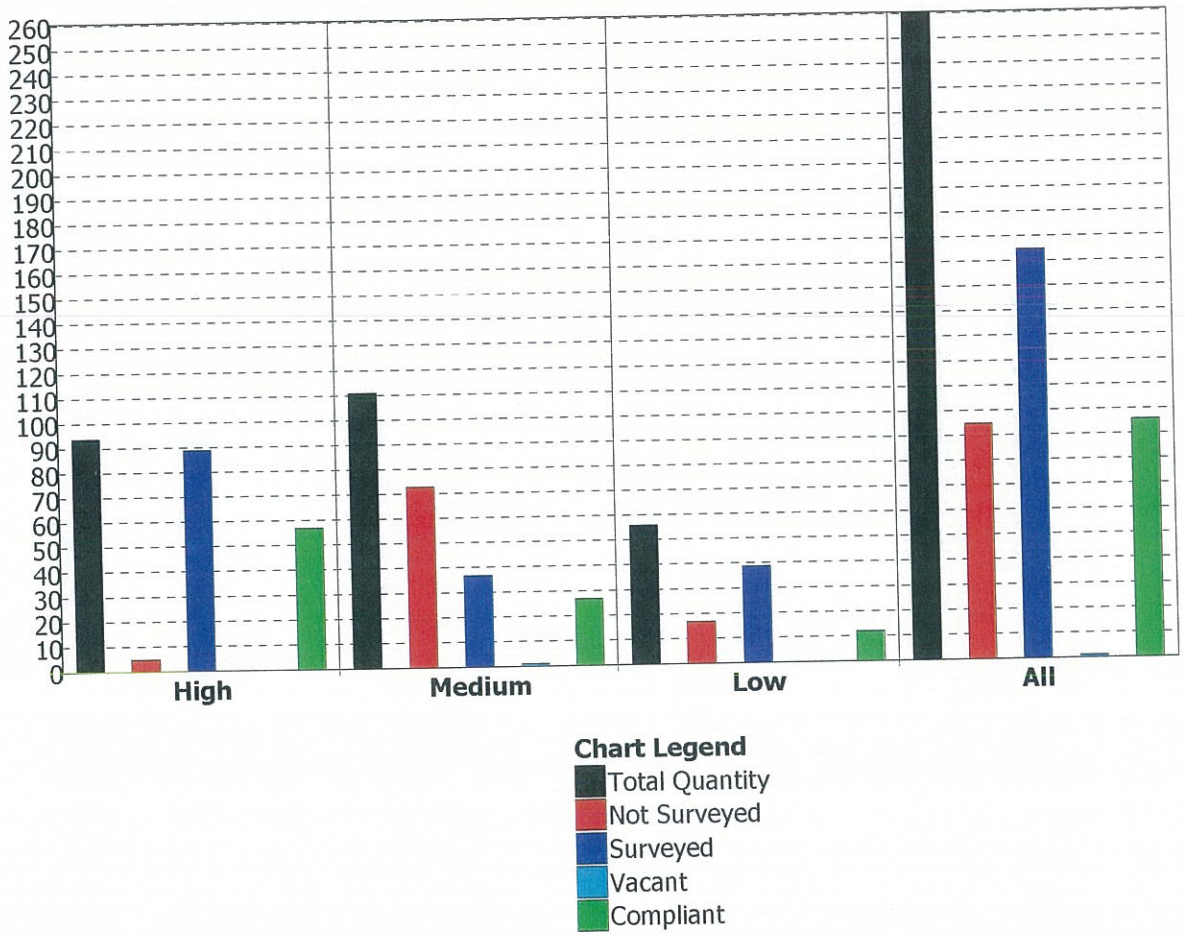

Existing Backflow Prevention Assemblies
Town of Osoyoos

1000.140	Osoyoos Secondary School			HS
Serial #	185135	**Test Due**	4/6/2012	
Location	Southside front of school irrigation			
Manufacturer	Watts	**Model**	709	
Type	DCVA	**Size**	4"	
Test History				
Test Date	4/1/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Rorie	**Tester #**	2081	
Test Date	5/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Rorie	**Tester #**	2081	
Test Date	4/6/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Bruce Porteous	**Tester #**	10475	
			Total Tests	3

114.125	Palms By The Lake			HSC
Serial #	37856	**Test Due**	1/11/2012	
Location	Parkade - irrigation			
Manufacturer	Watts	**Model**	007MIQT	
Type	DCVA	**Size**	2"	
Test History				
Test Date	12/12/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	**Tester #**	5341	
Test Date	1/4/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	12/8/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	12/9/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	12/21/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	12/21/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	1/11/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	7

Serial #	ZEL0107	**Test Due**	1/11/2012	
Location	Parkade - Mechincal - Fire Protection			
Manufacturer	Ames	**Model**	2000SS	
Type	DCVA	**Size**	4"	
Test History				
Test Date	12/13/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Kellandenk	**Tester #**	2452	
Test Date	12/8/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	12/9/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	12/21/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	1/11/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	

Existing Backflow Prevention Assemblies
Town of Osoyoos

114.125	Palms By The Lake			HSC
			Total Tests	5
Serial #	282165	**Test Due**	3/22/2011	
Location	Pool makeup			
Manufacturer	Watts	**Model**	009M3QT	
Type	RPBA	**Size**	3/4"	
	Test History			
Test Date	3/22/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	1

Existing Backflow Prevention Assemblies
Town of Osoyoos

1256.010	Waltons Mountain Resort			HSC
Serial #	05116	**Test Due**	10/13/2012	
Location	Pool makeup supply			
Manufacturer	Watts	**Model**	009M2QT	
Type	RP	**Size**	1 1/4"	
Test History				
Test Date	9/3/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Border Plumbing	**Tester #**	6443	
Test Date	9/28/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Rick Jones	**Tester #**	6172	
Test Date	10/13/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Rick Jones	**Tester #**	6172	
			Total Tests	3

Serial #	01063	**Test Due**	10/13/2012	
Location	Premise isolation on main			
Manufacturer	Conbraco	**Model**		
Type	DCVA	**Size**	3"	
Test History				
Test Date	9/3/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Border Plumbing	**Tester #**	6443	
Test Date	9/28/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Rick Jones	**Tester #**	6172	
Test Date	10/13/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Rick Jones	**Tester #**	6172	
			Total Tests	3

Existing Backflow Prevention Assemblies
Town of Osoyoos

1323.000	Island View RV			HSC
Serial #	NAA25	Test Due	11/25/2012	
Location	Premise isolation on main			
Manufacturer	Conbraco	Model	4020A02	
Type	DCVA	Size	4"	
Test History				
Test Date	11/25/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Craig Johnson	Tester #	6995	
Test Date	10/30/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Shawn Lawry	Tester #	6085	
			Total Tests	2

1326.000	Village on the Lake			HSC
Serial #	GD1589	Test Due	11/17/2012	
Location	Fire system supply - Verano mechanical room			
Manufacturer	Watts	Model	757	
Type	DCVA	Size	4"	
Test History				
Test Date	11/17/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Dale Grimes	Tester #	3632	
			Total Tests	1

Serial #	A09632	Test Due	11/17/2012	
Location	Mechanical room premise isolation			
Manufacturer	Watts	Model	007M1QT	
Type	RPBA	Size	2"	
Test History				
Test Date	11/17/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Dale Grimes	Tester #	3632	
			Total Tests	1

Serial #	3130153	Test Due	11/17/2012	
Location	Irrigation system supply			
Manufacturer	Wilkins	Model	950XL	
Type	DCVA	Size	1 1/2"	
Test History				
Test Date	11/17/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Dale Grimes	Tester #	3632	
			Total Tests	1

Serial #	U09974	Test Due	11/17/2012	
Location	Fire Supply - Sol Mechanical room			
Manufacturer	Wilkins	Model	350A	
Type	DCVA	Size	4"	
Test History				
Test Date	11/17/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Dale Grimes	Tester #	3632	
			Total Tests	1

1334.010a	OASIS R.V. PARK LTD.			HSC
Serial #	57436	Test Due	5/28/2012	
Location	Pool makeup supply			
Manufacturer	Watts	Model	007 M3 QT	
Type	DCVA	Size	3/4"	
Test History				
Test Date	5/28/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Doug Wilchynski	Tester #	10478	
			Total Tests	1

Serial #	XK371	Test Due	5/30/2012	
Location	Premise isolation on main			
Manufacturer	Apollo	Model	40108T1	
Type	DCVA	Size	2"	
Test History				
Test Date	5/30/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Dave Wilchynski	Tester #	10478	
			Total Tests	1

1348.102	Las Ventanas			HSC
Serial #	A5067	Test Due	8/3/2012	
Location	Geothermal makeup line			
Manufacturer	Watts	Model	009M3QT	
Type	RPBA	Size	3/4"	
Test History				
Test Date	9/29/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	8/3/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	2

Serial #	143616	Test Due	8/3/2012	
Location	Irrigation system supply			
Manufacturer	Watts	Model	007M1QT	
Type	DCVA	Size	1"	
Test History				
Test Date	2/16/2008	Test Result	☐ Failed	☑ Passed
Tester Name	Action Plumbing	Tester #	6985	
Test Date	9/29/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	8/3/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	3

Serial #	A01359	Test Due	8/3/2012	
Location	Mechanical room premise isolation			
Manufacturer	Watts	Model	007M2QT	
Type	DCVA	Size	1 1/2"	
Test History				
Test Date	2/16/2008	Test Result	☐ Failed	☑ Passed
Tester Name	Action Plumbing	Tester #	6085	
Test Date	9/29/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	

Existing Backflow Prevention Assemblies
Town of Osoyoos

1348.102	Las Ventanas			HSC
Test Date	8/3/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	3
Serial #	01344	**Test Due**	8/3/2012	
Location	Fire system supply			
Manufacturer	Conbraco	**Model**	4DC	
Type	DCVA	**Size**	4"	
	Test History			
Test Date	9/29/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	8/3/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	2

Existing Backflow Prevention Assemblies
Town of Osoyoos

1353.012	Walnut Beach Resort			HSC
Serial #	185294	**Test Due**	7/1/2012	
Location	Fire sprinkler - Parkade mechanical room			
Manufacturer	Watts	**Model**	709	
Type	DCVA	**Size**	4"	
	Test History			
Test Date	2/3/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	**Tester #**	1827	
Test Date	3/19/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	**Tester #**	1827	
Test Date	7/1/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dave Wilchynski	**Tester #**	10478	
			Total Tests	3

Serial #	277302	**Test Due**	7/14/2012	
Location	Swimming pool makeup - Replaced 110920			
Manufacturer	Watts	**Model**	009M2QTRP	
Type	RPBA	**Size**	2"	
	Test History			
Test Date	7/14/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dave wilchynski	**Tester #**	10478	
			Total Tests	1

Serial #	A24846	**Test Due**	7/14/2012	
Location	Boiler makeup supply			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1"	
	Test History			
Test Date	7/14/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dave Wilchynski	**Tester #**	10478	
			Total Tests	1

Serial #	A83972	**Test Due**	7/14/2012	
Location	Pool deck melter			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1"	
	Test History			
Test Date	7/14/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dave Wilchynski	**Tester #**	10478	
			Total Tests	1

Serial #	A12925	**Test Due**	3/30/2010
Location	Commercial laundry #1		
Manufacturer	Watts	**Model**	009M2QT
Type	RPBA	**Size**	1 1/2"

Serial #	A12306	**Test Due**	8/30/2011	
Location	Commercial laundry #2			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1 1/2"	
	Test History			
Test Date	7/1/2011	**Test Result**	☑ Failed	☐ Passed
Tester Name	Dave Wilchynski	**Tester #**	10478	

Existing Backflow Prevention Assemblies
Town of Osoyoos

1353.012	Walnut Beach Resort			HSC
			Total Tests	1
Serial #	12480	**Test Due**	7/20/2012	
Location	Commercial dishwasher			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	1/2"	
	Test History			
Test Date	7/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dave Wilchynski	**Tester #**	10478	
			Total Tests	1

Serial #	A83879	**Test Due**	7/20/2012	
Location	Outdoor water feature supply			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1"	
	Test History			
Test Date	7/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dave Wilchynski	**Tester #**	10478	
			Total Tests	1

Serial #	138667	**Test Due**	7/1/2012	
Location	Laundry HW at Washer (#1)			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1 1/2"	
	Test History			
Test Date	7/1/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dave Wilchynski	**Tester #**	10478	
			Total Tests	1

138.000	HUDSON (Riviera Motel)			MSC
Serial #	209578	**Test Due**	6/20/2012	
Location	Furnace room - Zone			
Manufacturer	Conbraco	**Model**	RP4A	
Type	RPBA	**Size**	3/4"	
	Test History			
Test Date	5/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
Test Date	6/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	2

Serial #	209520	**Test Due**	6/20/2012	
Location	Crawl space poolside - Premise Isolation			
Manufacturer	Conbraco	**Model**	RP4A	
Type	RPBA	**Size**	3/4"	
	Test History			
Test Date	5/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
Test Date	6/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	2

Serial #	195254	**Test Due**	6/20/2012	
Location	Laundry cold supply			
Manufacturer	Conbraco	**Model**	RP4A	
Type	RPBA	**Size**	1/2"	
	Test History			
Test Date	5/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveet	**Tester #**	5129	
Test Date	6/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	2

Serial #	195262	**Test Due**	6/20/2012	
Location	Laundry hot supply			
Manufacturer	Conbraco	**Model**	RP4A	
Type	RPBA	**Size**	1/2"	
	Test History			
Test Date	5/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
Test Date	6/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	2

Serial #	284809	**Test Due**	7/12/2012	
Location	Boiler makeup - replaced 195255			
Manufacturer	Conbraco	**Model**	RP4A	
Type	RPBA	**Size**	1/2"	
	Test History			
Test Date	7/12/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	1

Existing Backflow Prevention Assemblies
Town of Osoyoos

138.000	HUDSON (Riviera Motel)			MSC
Serial #	240348	**Test Due**	6/20/2012	
Location	Premise Isolation - laundry room crawlspace			
Manufacturer	Conbraco	**Model**	RP4A	
Type	RPBA	**Size**	1 1/2"	
Test History				
Test Date	5/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
Test Date	6/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	2

Serial #	255230	**Test Due**	7/12/2012	
Location	Laundry room hot - replaces 209609			
Manufacturer	Conbraco	**Model**	RP4A	
Type	RPBA	**Size**	3/4"	
Test History				
Test Date	7/12/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	1

138.010	DESIGN BURGER & DOGS INC. (Sage Pub)			HSC
Serial #	18568	**Test Due**	1/3/2012	
Location	Premise isolation			
Manufacturer	Watts	**Model**	009M3QT	
Type	RPBA	**Size**	3/4"	
Test History				
Test Date	7/28/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	1/3/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Wilchynski	**Tester #**	10478	
			Total Tests	2

290.010	550524 BC LTD. (Cottonwood Plaza)			HSC
Serial #	325648	**Test Due**	4/20/2012	
Location	2) Irrigation system supply in utility room - repalced 70437			
Manufacturer	Watts	**Model**	009 M3QT	
Type	RPBA	**Size**	3/4 inch	
Test History				
Test Date	4/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Wilchynski	**Tester #**	10478	
			Total Tests	1

Serial #	240431	**Test Due**	4/20/2012	
Location	East side of building under stairs			
Manufacturer	WATTS	**Model**	009 M2 QT	
Type	RP	**Size**	2 INCH	
Test History				
Test Date	1/19/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Vince Chapman	**Tester #**	5306	
Test Date	6/4/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	

Existing Backflow Prevention Assemblies
Town of Osoyoos

290.010	550524 BC LTD. (Cottonwood Plaza)			HSC
Test Date	5/4/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Followfield	Tester #	6443	
Test Date	5/11/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	4/20/2011	Test Result	☐ Failed	☑ Passed
Tester Name	David Wilchynski	Tester #	10478	
			Total Tests	5

290.110	THE DESERT MIRAGE			M
Serial #	127762	Test Due	3/29/2012	
Location	Fire Supply			
Manufacturer	Ames	Model	SS2000	
Type	DCVA	Size	4"	
	Test History			
Test Date	3/29/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Kevin Robinson	Tester #	7795	
			Total Tests	1

Serial #	75604	Test Due	3/29/2012	
Location	Pool Fountain Supply			
Manufacturer	Watts	Model	007M2QT	
Type	DCVA	Size	1 1/2"	
	Test History			
Test Date	3/29/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Kevin Robinson	Tester #	7795	
			Total Tests	1

314.000	SALIN HOLDINGS INC. (Dairy Queen)			HSC
Serial #	A91892	Test Due	11/16/2012	
Location	Premise isolation on main			
Manufacturer	Watts	Model	007M1QT	
Type	DCVA	Size	1"	
	Test History			
Test Date	8/6/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	Tester #	6443	
Test Date	11/10/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	11/16/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
			Total Tests	3

Existing Backflow Prevention Assemblies
Town of Osoyoos

321.200	551996 BC LTD (BEST WESTERN)			HSC
Serial #	B02705	Test Due	5/16/2012	
Location	Pool Makeup supply			
Manufacturer	Watts	Model	009M2QT	
Type	RPBA	Size	1/2"	
Test History				
Test Date	2/6/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	Tester #	6085	
Test Date	5/16/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Brad Westen	Tester #	4364	
			Total Tests	2

Serial #	A18734	Test Due	5/16/2012	
Location	Laundry room supply #1			
Manufacturer	Watts	Model	009M2QT	
Type	RPBA	Size	1 1/4"	
Test History				
Test Date	3/6/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	Tester #	6085	
Test Date	5/16/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Brad Westen	Tester #	4364	
			Total Tests	2

Serial #	227848	Test Due	5/16/2012	
Location	LAundry supply #2			
Manufacturer	Apollo	Model	RP4A	
Type	RPBA	Size	1 1/4"	
Test History				
Test Date	3/6/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	Tester #	6085	
Test Date	5/16/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Brad Westen	Tester #	4364	
			Total Tests	2

Serial #	B33454	Test Due	5/16/2012	
Location	Pool and spa room			
Manufacturer	Watts	Model	009 M3 QT	
Type	RPBA	Size	3/4"	
Test History				
Test Date	2/6/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	Tester #	6085	
Test Date	5/16/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Brad Westen	Tester #	4364	
			Total Tests	2

Serial #	2BN0069	Test Due	5/16/2012	
Location	Fire sprinkler in water entry room			
Manufacturer	Ames	Model	2000 SS	
Type	DCVA	Size	3 inch	
Test History				
Test Date	4/3/2007	Test Result	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	Tester #	1827	

321.200	551996 BC LTD (BEST WESTERN)			HSC
Test Date	11/23/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Robinson	**Tester #**	7795	
Test Date	5/16/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Brad Westen	**Tester #**	4364	
			Total Tests	3
Serial #	257915	**Test Due**	5/16/2012	
Location	Irrigation in water entry room			
Manufacturer	Apollo	**Model**	DC4A	
Type	DCVA	**Size**	2 inch	
Test History				
Test Date	5/16/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Brad Westen	**Tester #**	4364	
			Total Tests	1

338.005	SAFARI BEACH RESORT LTD.			HSC
Serial #	180843	**Test Due**	4/6/2012	
Location	Room C Utility premise isolation			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	2"	
Test History				
Test Date	4/6/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	1

Serial #	180852	**Test Due**	4/6/2012	
Location	Irrigation supply main			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	2"	
Test History				
Test Date	4/6/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	1

345.105	HUSKY OIL OPERATIONS LTD.			HSC
Serial #	256955	**Test Due**	7/16/2010	
Location	Upstairs Mechanical Room #1			
Manufacturer	WATTS	**Model**	009 M2 QT	
Type	RP	**Size**	2 INCH	
Test History				
Test Date	1/20/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Vince Chapman	**Tester #**	5306	
Test Date	7/16/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Followfield	**Tester #**	6443	
Test Date	7/31/2010	**Test Result**	☑ Failed	☐ Passed
Tester Name	Action Plumbing	**Tester #**	6085	
			Total Tests	3

345.105	HUSKY OIL OPERATIONS LTD.			HSC
Serial #	296352	**Test Due**	1/20/2007	
Location	Ice Machine By Office			
Manufacturer	WATTS	**Model**	009	
Type	RP	**Size**	1/2 INCH	
	Test History			
Test Date	1/20/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Vince Chapman	**Tester #**	5306	
			Total Tests	1

Serial #	301517	**Test Due**	7/16/2010	
Location	Upstairs Mechanical Room #12			
Manufacturer	WATTS	**Model**	009 QT	
Type	RPBA	**Size**	1/2 inch	
	Test History			
Test Date	1/26/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Vince Chapman	**Tester #**	5306	
Test Date	7/16/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Followfield	**Tester #**	6443	
			Total Tests	2

Serial #	296387	**Test Due**	1/9/2007	
Location	Store (Back area)			
Manufacturer	WATTS	**Model**	009	
Type	RPBA	**Size**	1/2 inch	
	Test History			
Test Date	1/9/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Vince Chapman	**Tester #**	5306	
			Total Tests	1

Serial #	231790	**Test Due**	1/9/2007	
Location	Mechanical Room serves the steam cleaner #34			
Manufacturer	WATTS	**Model**	009 M3 QT	
Type	RP	**Size**	3/4 inch	
	Test History			
Test Date	1/9/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Vince Chapman	**Tester #**	5306	
			Total Tests	1

Serial #	289877	**Test Due**	8/28/2011	
Location	Upstairs mechanical room #38 serves swamp cooler			
Manufacturer	WATTS	**Model**	009 QT	
Type	RP	**Size**	1/2 inch	
	Test History			
Test Date	1/18/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Vince Chapman	**Tester #**	5306	
Test Date	7/16/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Followfield	**Tester #**	6443	
Test Date	8/28/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Action Plumbing	**Tester #**	6085	
			Total Tests	3

Existing Backflow Prevention Assemblies
Town of Osoyoos

345.105	HUSKY OIL OPERATIONS LTD.			HSC
Serial #	W02436	**Test Due**	7/16/2010	
Location	Lock Box by Sani Dump			
Manufacturer	Watts	**Model**	00SQT	
Type	RPBA	**Size**	1/2"	
Test History				
Test Date	7/16/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Followfield	**Tester #**	6443	
			Total Tests	1

Serial #	373640	**Test Due**	8/16/2012	
Location	Sani Dump (replacement)			
Manufacturer	Watts	**Model**	009M3QT	
Type	RPBA	**Size**	3/4"	
Test History				
Test Date	8/16/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Wilchynski	**Tester #**	10478	
			Total Tests	1

Serial #	283391	**Test Due**	8/28/2011	
Location	Premise Isolation			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	2"	
Test History				
Test Date	8/28/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Action Plumbing	**Tester #**	6085	
			Total Tests	1

345.163	FODEY			HSC
Serial #	A04981	Test Due	5/28/2008	
Location	On North Wall			
Manufacturer	WATTS	Model	009M3	
Type	RPBA	Size	3/4	
Test History				
Test Date	6/21/2006	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	5/28/2007	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
			Total Tests	2

345.400	Mariposa Gardens - Baltic Properties Ltd.			HSC
Serial #	05386	Test Due	11/8/2012	
Location	Boiler room premise isolated			
Manufacturer	Conbraco	Model	DC	
Type	DCVA	Size	4"	
Test History				
Test Date	9/3/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	Tester #	6443	
Test Date	11/8/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
Test Date	12/16/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	Tester #	1827	
			Total Tests	3

Serial #	H63038	Test Due	11/8/2012	
Location	Fire system supply			
Manufacturer	Ames	Model		
Type	DCVA	Size	4"	
Test History				
Test Date	11/8/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
Test Date	9/3/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	Tester #	6443	
Test Date	11/23/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	2199	
			Total Tests	3

Serial #	A93008	Test Due	11/8/2012	
Location	Cooling tower makeup			
Manufacturer	Watts	Model	009M3QT	
Type	RPBA	Size	3/4"	
Test History				
Test Date	11/8/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
Test Date	9/3/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	Tester #	6443	
Test Date	12/16/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	Tester #	1827	
			Total Tests	3

Town of Osoyoos

347.010	Buy Low Foods			HSC
Serial #	FH2290	**Test Due**	8/3/2012	
Location	Mechanical room fire system			
Manufacturer	Watts	**Model**	757	
Type	DCVA	**Size**	4"	
Test History				
Test Date	10/9/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	9/7/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	8/3/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	3

Serial #	251343	**Test Due**	8/3/2012	
Location	Mechanical room premise			
Manufacturer	Watts	**Model**	099M2QT	
Type	RP	**Size**	2"	
Test History				
Test Date	10/9/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	9/7/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	8/3/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	3

347.210	MP Hospitality Ltd (Ridge Pub / Westridge Motor)			HSC
Serial #	133963	Test Due	5/20/2011	
Location	9) Boiler makeup line in boiler room			
Manufacturer	Watts	Model	007M2 QT	
Type	RPBA	Size	3/4 inch	
Test History				
Test Date	5/11/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	Tester #	6443	
Test Date	5/20/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
			Total Tests	2

Serial #	2KM1903	Test Due	9/29/2012	
Location	2) Fire system supply downstairs in utility room			
Manufacturer	Ames	Model	2000SS	
Type	DCVA	Size	4 inch	
Test History				
Test Date	9/10/2009	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	10/10/2004	Test Result	☑ Failed	☐ Passed
Tester Name		Tester #		
Test Date	9/7/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	9/29/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	4

Serial #	A04885	Test Due	5/20/2011	
Location	Mechanical room serves Irrigation			
Manufacturer	WATTS	Model	007M2QT	
Type	DCVA	Size	1 1/2	
Test History				
Test Date	6/6/2007	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	5/20/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
			Total Tests	2

Serial #	107362	Test Due	5/20/2011	
Location	Mechanical Room - Main Line			
Manufacturer	WATTS	Model	009M2QT	
Type	RPBA	Size	2"	
Test History				
Test Date	6/6/2007	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	5/11/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	Tester #	6443	
Test Date	5/20/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
			Total Tests	3

Existing Backflow Prevention Assemblies
Town of Osoyoos

347.210	MP Hospitality Ltd (Ridge Pub / Westridge Motor)			HSC
Serial #	101954	**Test Due**	5/20/2011	
Location	Pool Room/Mechanical			
Manufacturer	WATTS	**Model**	009M2QT	
Type	RPBA	**Size**	1 1/2	
Test History				
Test Date	1/10/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Vince Chapman	**Tester #**	5306	
Test Date	6/6/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	**Tester #**	6443	
Test Date	5/20/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	4

Serial #	258529	**Test Due**	5/20/2011	
Location	In mechanical room (premise iso)			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	2 inch	
Test History				
Test Date	6/6/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/20/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	2

Existing Backflow Prevention Assemblies
Town of Osoyoos

348.015	CANTER HOLDINGS LTD - 711 Store			MSC
Serial #	63145	**Test Due**	1/13/2012	
Location	4) Water filter on line to drink dispensor island			
Manufacturer	Watts	**Model**	007M1 QT	
Type	DCVA	**Size**	1 inch	
	Test History			
Test Date	12/7/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	1/13/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Chad Newfeld	**Tester #**	8439	
			Total Tests	2

Serial #	180842	**Test Due**	3/31/2012	
Location	Utility room premise isolation			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	2"	
	Test History			
Test Date	3/31/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	1

348.025	509888 BC LTD. (A & W)			HSC
Serial #	B18030	**Test Due**	2/17/2012	
Location	Irrigation system			
Manufacturer	Watts	**Model**	007M3QT	
Type	DCVA	**Size**	3/4"	
	Test History			
Test Date	10/15/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	**Tester #**	6443	
Test Date	2/17/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Soare	**Tester #**	2078	
			Total Tests	2

Serial #	A54345	**Test Due**	2/17/2012	
Location	Cooler compressor makeup			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1/2"	
	Test History			
Test Date	10/15/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	**Tester #**	6443	
Test Date	2/17/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Soare	**Tester #**	2078	
			Total Tests	2

348.075	MCDONALD'S RESTAURANTS OF			HSC
Serial #	A44114	**Test Due**	12/14/2011	
Location	Premise isolation			
Manufacturer	Watts	**Model**	2"	
Type	DCVA	**Size**	2"	
Test History				
Test Date	7/29/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Followfield	**Tester #**	6443	
Test Date	12/14/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	2

Serial #	B181105	**Test Due**	8/31/2010	
Location	Washer/steamer			
Manufacturer	Watts	**Model**	007M3QT	
Type	RPBA	**Size**	3/4"	
Test History				
Test Date	8/31/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	**Tester #**	6443	
			Total Tests	1

Serial #	1253609	**Test Due**	7/22/2010	
Location	Postmix beverage machine			
Manufacturer	Wilkins	**Model**	975XL	
Type	RPBA	**Size**	3/4 inch	
Test History				
Test Date	7/22/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	**Tester #**	6443	
			Total Tests	1

Existing Backflow Prevention Assemblies
Town of Osoyoos

348.150	RCMP			MSC
Serial #	A05415	**Test Due**	8/23/2012	
Location	Irrigation supply in staff washroom			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	1"	
	Test History			
Test Date	7/29/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
Test Date	7/23/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Wyatt Keogh	**Tester #**	10188	
Test Date	8/23/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Chad Neufeld	**Tester #**	8439	
			Total Tests	3

398.010	Osoyoos Super 8			HSC
Serial #	A87873	**Test Due**	7/23/2011	
Location	Pool makeup supply			
Manufacturer	Watts	**Model**	007 M1 QT	
Type	RP	**Size**	1"	
	Test History			
Test Date	7/23/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	1

Serial #	330243	**Test Due**	3/28/2012	
Location	In Pool Room			
Manufacturer	Watts	**Model**	009M3QT	
Type	RPBA	**Size**	1'	
	Test History			
Test Date	9/27/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	3/28/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	2

Serial #	107596	**Test Due**	3/28/2012	
Location	West Wing premise isolation			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
	Test History			
Test Date	3/28/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	1

Serial #	107599	**Test Due**	3/28/2012	
Location	East Wing premise isolation			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
	Test History			
Test Date	3/28/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	1

Existing Backflow Prevention Assemblies
Town of Osoyoos

443.000	Osoyoos Nursery School			MSC
Serial #	9609051301	**Test Due**	5/10/2012	
Location	Fire Protection - lower floor Mech Room			
Manufacturer	Febco	**Model**	805YD	
Type	DCVA	**Size**	3"	
	Test History			
Test Date	4/19/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	3/14/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	3/3/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	**Tester #**	5341	
Test Date	3/23/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	4/19/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	5/10/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	6

515.000	Sun Bowl Arena			HS
Serial #	218584	**Test Due**	6/28/2012	
Location	Back bay			
Manufacturer	Watts	**Model**	009 M3 QT	
Type	RPBA	**Size**	3/4 inch	
	Test History			
Test Date	4/22/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	6/28/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	3

535.112	RICHTER - NAPA Phonix Auto Parts			HSC
Serial #	A01989	**Test Due**	5/19/2012	
Location	In basement Premise Isolation			
Manufacturer	Watts	**Model**	007 M3	
Type	DCVA	**Size**	3/4inch	
	Test History			
Test Date	4/23/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	4/21/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/19/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	4

Existing Backflow Prevention Assemblies
Town of Osoyoos

535.250	TEJAY			HSC
Serial #	W190230	**Test Due**	2/15/2007	
Location	MAIN BOILER ROOM			
Manufacturer	WILKINS ZURN	**Model**	975XL	
Type	RP	**Size**	2"	
	Test History			
Test Date	2/15/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	VINCE CHAPMAN	**Tester #**	5306	
			Total Tests	1

55.005	Ambrosia Restraunt			MSC
Serial #	263139	**Test Due**	11/10/2011	
Location	Premise Isolation in storage room			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1"	
	Test History			
Test Date	8/4/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	11/10/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	2

573.340	Interior Health (Sagebrush Lodge)			MSC
Serial #	1169400	**Test Due**	10/15/2011	
Location	Irrigation supply			
Manufacturer	Wilkins	**Model**	950XL	
Type	DCVA	**Size**	1 1/2"	
	Test History			
Test Date	9/10/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	10/15/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	2

Serial #	LB0078	**Test Due**	12/5/2012	
Location	Basement valve room - serves fire protection			
Manufacturer	Watts	**Model**	757 DC	
Type	DCVA	**Size**	6"	
	Test History			
Test Date	12/5/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Morris Weremchuk	**Tester #**	10193	
Test Date	3/17/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Morris Weremchuk	**Tester #**	10193	
			Total Tests	2

573.745	Greycon Homes Ltd			M
Serial #	B23290	**Test Due**	8/4/2010	
Location	Irrigation supply			
Manufacturer	Watts	**Model**	007M3QT	
Type	DCVA	**Size**	3/4"	
	Test History			
Test Date	8/4/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	**Tester #**	6443	
			Total Tests	1

575.000	La Mirada			HSC
Serial #	1716981008	**Test Due**	1/26/2012	
Location	Fire Sprinkler system			
Manufacturer	Watts	**Model**	774	
Type	DCVA	**Size**	4"	
	Test History			
Test Date	7/29/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
Test Date	1/26/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
			Total Tests	2

Serial #	219910	**Test Due**	1/26/2012	
Location	Premise isolation on main			
Manufacturer	Watts	**Model**	909RP	
Type	RPBA	**Size**	4"	
	Test History			
Test Date	7/29/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
Test Date	1/26/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
			Total Tests	2

Serial #	A02300	**Test Due**	1/26/2012	
Location	Irrigation supply			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
	Test History			
Test Date	7/29/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
Test Date	1/26/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
			Total Tests	2

Serial #	A08214	**Test Due**	1/26/2012	
Location	Boiler makeup supply			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1"	
	Test History			
Test Date	7/29/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
Test Date	1/26/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	

575.000	La Mirada	HSC
	Total Tests	2

6019.010	Okanagan Tree Fruit Coop - Monashee Packing House			HSC
Serial #	C1979	Test Due	4/28/2011	
Location	Premise isolation on main in valve pit			
Manufacturer	Febco	Model	805Y	
Type	DCVA	Size	2"	

Serial #	318133	Test Due	6/6/2012	
Location	Fire sprinkler priming line			
Manufacturer	Apollo	Model	DC4A	
Type	DCVA	Size	3/4"	
Test History				
Test Date	6/6/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	1

Serial #	296211	Test Due	6/6/2012	
Location	Premise isolation in palnt			
Manufacturer	Watts	Model	009M2QT	
Type	RPBA	Size	2"	
Test History				
Test Date	6/6/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	1

6027.000	Sandhu Green Houses - Harjeewa / Jasvir Sandhu			HS
Serial #	3309959	Test Due	4/28/2011	
Location	Greenhouse system supply			
Manufacturer	Wilkins	Model	950 XL	
Type	DCVA	Size	2"	

6078.010	DEOL BROS. FARMS LTD. (Shell)			HSC
Serial #	186274	Test Due	4/12/2012	
Location	Premise Isolation			
Manufacturer	Watts	Model	007M3QT	
Type	DCVA	Size	3/4"	
Test History				
Test Date	4/12/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Jeremy Haines	Tester #	7362	
			Total Tests	1

62.000	HUDSON (Poplars Motel)			MSC
Serial #	209609	**Test Due**	6/20/2012	
Location	Laundry (Lower)			
Manufacturer	Conbraco	**Model**	RP4A	
Type	RPBA	**Size**	3/4"	
Test History				
Test Date	5/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maverty	**Tester #**	5129	
Test Date	6/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	2

Serial #	209573	**Test Due**	6/20/2012	
Location	Laundry (Upper)			
Manufacturer	Conbraco	**Model**	RP4A	
Type	RPBA	**Size**	3/4"	
Test History				
Test Date	5/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
Test Date	6/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	2

Serial #	160641	**Test Due**	6/20/2012	
Location	Premise Isolation - Basement			
Manufacturer	Conbraco	**Model**	DC4A	
Type	DCVA	**Size**	1"	
Test History				
Test Date	5/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
Test Date	6/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	2

Serial #	160759	**Test Due**	6/20/2012	
Location	Irrigation - back grass			
Manufacturer	Conbraco	**Model**	DC4A	
Type	DCVA	**Size**	1"	
Test History				
Test Date	5/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
Test Date	6/20/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Ken Raine	**Tester #**	2830	
			Total Tests	2

Existing Backflow Prevention Assemblies
Town of Osoyoos

623.000	SOUTHERN OKANAGAN - Double O Bikes			LSC
Serial #	3358551	**Test Due**	11/10/2012	
Location	Premise isolation on main service			
Manufacturer	Wilkins	**Model**	950XL	
Type	DCVA	**Size**	3/4"	
	Test History			
Test Date	10/21/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Soare	**Tester #**	2078	
Test Date	11/10/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Soare	**Tester #**	2078	
			Total Tests	2

624.010	Tim Hortons			MSC
Serial #	142891	**Test Due**	4/15/2012	
Location	On main waterline in staff washroom.			
Manufacturer	Watts	**Model**	007 M1 QT	
Type	DCVA	**Size**	2"	
	Test History			
Test Date	1/20/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	Winter Plumbing	**Tester #**	5662	
Test Date	8/5/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	1/29/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
Test Date	4/15/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	4

Serial #	306678	**Test Due**	4/15/2012	
Location	On irrigation line in staff washroom			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	1 inch	
	Test History			
Test Date	1/20/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	Doug Tough	**Tester #**	5662	
Test Date	8/5/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	1/29/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
Test Date	4/15/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	4

Existing Backflow Prevention Assemblies
Town of Osoyoos

638.000	HOWARD'S SERVICE LTD			HSC
Serial #	236681	**Test Due**	8/16/2012	
Location	Under Coffee Counter			
Manufacturer	WATTS	**Model**	099 M3	
Type	RPBA	**Size**	3/4 INCH	
	Test History			
Test Date	5/4/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	**Tester #**	6443	
Test Date	7/31/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	**Tester #**	6085	
Test Date	8/16/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Wilchynski	**Tester #**	10478	
			Total Tests	3

Serial #	290482	**Test Due**	8/16/2012	
Location	Under Coffee machine services Sani Dump			
Manufacturer	WATTS	**Model**	009	
Type	RP	**Size**	1/2 INCH	
	Test History			
Test Date	8/16/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Wilchynski	**Tester #**	10478	
Test Date	1/10/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Vince Chapman	**Tester #**	5306	
Test Date	5/4/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	**Tester #**	6443	
Test Date	7/31/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	**Tester #**	6085	
Test Date	8/16/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Wilchynski	**Tester #**	10478	
			Total Tests	5

Serial #	23004D	**Test Due**	7/31/2011	
Location	Under Sink fixture protected main line			
Manufacturer	WATTS	**Model**	009	
Type	RP	**Size**	3/4 Inch	
	Test History			
Test Date	1/4/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Vince Chapman	**Tester #**	5306	
Test Date	7/31/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	**Tester #**	6085	
			Total Tests	2

Existing Backflow Prevention Assemblies
Town of Osoyoos

64.000	DESERT PROPERTIES LTD (Coast Hotel)			HSC
Serial #	26950	**Test Due**	12/9/2011	
Location	Premise - southwest corner of basement			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1 1/2"	
	Test History			
Test Date	12/7/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	12/9/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	2

Serial #	28477	**Test Due**	12/9/2011	
Location	Premise - South east corner of basement			
Manufacturer	Watts	**Model**	009RP	
Type	RPBA	**Size**	3"	
	Test History			
Test Date	12/7/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	12/9/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	2

641.010	INTERIOR PROJECTS INC (Smitty's)			HSC
Serial #	TH679	**Test Due**	5/31/2012	
Location	Premise isolation on main with DCVA - no drainage for RPBA			
Manufacturer	Conbraco	**Model**	40104T2	
Type	DCVA	**Size**	3/4"	
	Test History			
Test Date	5/27/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/31/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	2

645.000	TOWN OF OSOYOOS (TOWN HALL) / Fire Hall			HSC
Serial #	23533	**Test Due**	7/18/2012	
Location	Premise Iso - under south stairs			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1 1/2"	
	Test History			
Test Date	7/18/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/12/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/18/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	3

645.000	TOWN OF OSOYOOS (TOWN HALL) / Fire Hall			HSC
Serial #	23335	**Test Due**	7/18/2012	
Location	Premise isolation			
Manufacturer	Watts	**Model**	007M3QT	
Type	DCVA	**Size**	3/4"	
	Test History			
Test Date	7/18/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/12/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/18/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	3

657.000	PENDERGRAFT PROFESSIONAL			HSC
Serial #	141236	**Test Due**	8/9/2012	
Location	Fixture (Dental pump) above hot water tank in basement			
Manufacturer	Watts	**Model**	009QT	
Type	RPBA	**Size**	1/2	
	Test History			
Test Date	2/22/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	Nick Hebig	**Tester #**	6177	
Test Date	3/6/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/19/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/9/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/22/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	8/9/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	6

Serial #	190541	**Test Due**	8/9/2012	
Location	Premises - in crawl space above main water supply			
Manufacturer	Watts	**Model**	009 M3 QT	
Type	RPBA	**Size**	3/4	
	Test History			
Test Date	3/6/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/19/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/9/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/22/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	8/9/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	5

68.000	THE OWNERS (Holiday Inn)			HSC
Serial #	9609251240	**Test Due**	3/9/2012	
Location	2) Fire system supply mechanical room			
Manufacturer	Febco	**Model**	805YD	
Type	DCVA	**Size**	4 inch	
Test History				
Test Date	9/10/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	10/3/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	10/8/2004	**Test Result**	☑ Failed	☐ Passed
Tester Name	John S.	**Tester #**	Accurate Fire Pro	
Test Date	10/10/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	3/14/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	12/9/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	3/23/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	3/23/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	7845	
Test Date	3/9/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	9

Serial #	23174	**Test Due**	3/9/2012	
Location	3) Irrigation system supply off main in mechanical room			
Manufacturer	Watts	**Model**	007M2 QT	
Type	DCVA	**Size**	11/2 inch	
Test History				
Test Date	5/13/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	3/23/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	7845	
Test Date	3/9/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	3

Serial #	113866	**Test Due**	3/9/2012	
Location	8) Existing Double Check Valve Assembly in pool room at 7)			
Manufacturer	Watts	**Model**	007M2 QT	
Type	DCVA	**Size**	3/4 inch	
Test History				
Test Date	3/23/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	7845	
Test Date	3/9/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	2

68.000	THE OWNERS (Holiday Inn)			HSC
Serial #	106715	**Test Due**	3/9/2012	
Location	61) Boiler makeup line in boiler room 3rd floor 2-B- replaced			
Manufacturer	Watts	**Model**	007M2 QT	
Type	DCVA	**Size**	3/4 inch	
	Test History			
Test Date	5/13/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	3/23/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	7845	
Test Date	3/9/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	3

Serial #	185660	**Test Due**	3/9/2012
Location	Parkade Mechanical room - Premise isolation		
Manufacturer	Watts	**Model**	709
Type	DCVA	**Size**	4 inch
	Test History		
Test Date	5/13/2009	**Test Result**	☐ Failed ☑ Passed
Tester Name	John Samuelson	**Tester #**	2452
Test Date	3/9/2011	**Test Result**	☐ Failed ☑ Passed
Tester Name	Galen Bond	**Tester #**	7845
			Total Tests 2

71.000	SAIRAM HOLDINGS LTD. - Spanish Fiesta Resort			HSC
Serial #	342131	**Test Due**	5/28/2012	
Location	Premise isolation - water softner room - Fiesta			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1"	
	Test History			
Test Date	5/28/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dave Wilchynski	**Tester #**	10478	
			Total Tests	1

Serial #	325649	**Test Due**	5/28/2012
Location	Premise isolation on main - Falcon #1		
Manufacturer	Watts	**Model**	009M3QT
Type	RPBA	**Size**	3/4"
	Test History		
Test Date	5/28/2011	**Test Result**	☐ Failed ☑ Passed
Tester Name	Dave Wilchynski	**Tester #**	10478
			Total Tests 1

Serial #	325664	**Test Due**	5/28/2012
Location	Premise isolation - Falcon main #2		
Manufacturer	Watts	**Model**	009M3QT
Type	RPBA	**Size**	3/4"
	Test History		
Test Date	5/28/2011	**Test Result**	☐ Failed ☑ Passed
Tester Name	Dave Wilchynski	**Tester #**	10478
			Total Tests 1

Existing Backflow Prevention Assemblies
Town of Osoyoos

714 06249.010	LLoyd Sauder		AGNS
Serial #	2655915	Test Due	6/24/2009
Location	irrigation system		
Manufacturer	Wilkins	Model	975xl
Type	RPBA	Size	2 inch

714.06262.000	Gurpiar Aulakh and Roop Sing Smagh		HSAGRI
Serial #	2310939	Test Due	6/24/2009
Location	irrigation system		
Manufacturer	Wilkins	Model	975xl
Type	RPBA	Size	2 inch

714.6265.000	Layden Vineyards		HSC
Serial #	10772	Test Due	6/10/2010
Location	Premise Isolation south west corner		
Manufacturer	Watts	Model	007 DC
Type	DCVA	Size	3"
Test History			
Test Date	6/10/2009	Test Result	☐ Failed ☑ Passed
Tester Name	Howard Hebig	Tester #	6614
		Total Tests	1

714.6330.000	BUCK, DAVID		M
Serial #	FV602	Test Due	5/6/2007
Location	MID PROPERTY		
Manufacturer	CONBRACO	Model	40208A2
Type	RPBA	Size	2
Test History			
Test Date	5/6/2006	Test Result	☐ Failed ☑ Passed
Tester Name	LANCE SOARE	Tester #	2078
		Total Tests	1

758.000	CALDER (Osoyoos Medical Clinic)		MSC
Serial #	187215	Test Due	6/1/2012
Location	Premises - directly inside crawl space		
Manufacturer	Watts	Model	009M3QT
Type	RPBA	Size	3/4
Test History			
Test Date	2/16/2005	Test Result	☐ Failed ☑ Passed
Tester Name	Nick Hebig	Tester #	6177
Test Date	3/6/2006	Test Result	☐ Failed ☑ Passed
Tester Name	Howard Hebig	Tester #	6614
Test Date	6/8/2007	Test Result	☐ Failed ☑ Passed
Tester Name	Howard Hebig	Tester #	6614
Test Date	5/4/2009	Test Result	☐ Failed ☑ Passed
Tester Name	Howard Hebig	Tester #	6614
Test Date	5/11/2010	Test Result	☐ Failed ☑ Passed
Tester Name	Howard Hebig	Tester #	6614
Test Date	6/1/2011	Test Result	☐ Failed ☑ Passed
Tester Name	Craig Johnson	Tester #	6995

Existing Backflow Prevention Assemblies
Town of Osoyoos

758.000	CALDER (Osoyoos Medical Clinic)			MSC
			Total Tests	6
Serial #	156404	**Test Due**	6/1/2012	
Location	Zone - directly inside crawlspace			
Manufacturer	Watts	**Model**	007M3-QT	
Type	DCVA	**Size**		
	Test History			
Test Date	2/16/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	Nick Hebig	**Tester #**	6177	
Test Date	3/6/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	6/8/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/4/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	6/1/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	6

769.005	Breeze Bar and Grill			HS
Serial #	2DL0824	Test Due	6/18/2010	
Location	2) Fire system supply in electrical room in basement			
Manufacturer	Ames	Model	2000SS	
Type	DCVA	Size	4 inch	
Test History				
Test Date	6/18/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Brad Westen	Tester #	4364	
			Total Tests	1

77.000	Desert Surfside			MSC
Serial #	1428760205	Test Due	9/29/2012	
Location	Sprinkler room in front of elevator Main Floor			
Manufacturer	Ames	Model	2000SS	
Type	DCVA	Size	4"	
Test History				
Test Date	10/1/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Gaien Bond	Tester #	7845	
Test Date	11/30/2006	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	Tester #	5341	
Test Date	10/15/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	9/29/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	4

Serial #	137896	Test Due	9/29/2012	
Location	Sprinkler valve room Main Floor in front of elevator main isolation			
Manufacturer	Watts	Model	007M1OT	
Type	DCVA	Size	2"	
Test History				
Test Date	11/30/2006	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	Tester #	5341	
Test Date	6/10/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Josh Bonell	Tester #	8123	
Test Date	1/11/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	9/29/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	4

Serial #	170817	Test Due	1/11/2012	
Location	Mechanical room in front of elevator irrigation system			
Manufacturer	Watts	Model	007M3QT	
Type	DCVA	Size	3/4 inch	
Test History				
Test Date	11/30/2006	Test Result	☑ Failed	☐ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	6/10/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Josh Bonell	Tester #	8123	
Test Date	1/11/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	

77.000	Desert Surfside			MSC
			Total Tests	3

772.016	White Sands Strata Corp - KAS1462			HSC
Serial #	05182	**Test Due**	9/6/2012	
Location	Level 1 Mech Rm 7803 (Replacement?)			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
	Test History			
Test Date	10/1/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	10/17/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	**Tester #**	5341	
Test Date	9/16/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	9/6/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	4

Serial #	493733	**Test Due**	9/6/2012	
Location	1. Valve room - serves irrigation - Phase III			
Manufacturer	Wilkins	**Model**	950XL	
Type	DCVA	**Size**	1 1/2"	
	Test History			
Test Date	10/1/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	10/17/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	**Tester #**	5341	
Test Date	11/25/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	9/16/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	9/6/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	5

Serial #	01461	**Test Due**	9/6/2012	
Location	2. valve room - serves fire protection - Phase I			
Manufacturer	Watts	**Model**	770	
Type	DCVA	**Size**	4"	
	Test History			
Test Date	10/1/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	10/3/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	10/17/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	**Tester #**	5341	
Test Date	11/25/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	9/16/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	

Existing Backflow Prevention Assemblies
Town of Osoyoos

772.016	White Sands Strata Corp - KAS1462			HSC
Test Date	9/6/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	6
Serial #	08883	Test Due	9/6/2012	
Location	3.Valve Room - serves irrigation - Phase I			
Manufacturer	Watts	Model	007M1QT	
Type	DCVA	Size	1 1/2"	
Test History				
Test Date	10/1/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	10/3/2006	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	10/17/2007	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	Tester #	5341	
Test Date	11/25/2008	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	9/16/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	9/6/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	6

Serial #	2DJ0750	Test Due	9/6/2012	
Location	Level 1 Mechanical room - Fire system			
Manufacturer	Ames	Model	2000SS	
Type	DCVA	Size	4 inch	
Test History				
Test Date	10/1/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Galem Bond	Tester #	7845	
Test Date	10/3/2006	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	10/17/2007	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	Tester #	5341	
Test Date	11/25/2008	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	9/16/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	9/6/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	6

Existing Backflow Prevention Assemblies
Town of Osoyoos

776.001	Watermark Resorts			HSC
Serial #	B22478	**Test Due**	1/27/2012	
Location	Boiler Makeup supply 1st floor mechanical room			
Manufacturer	Watts	**Model**	009M3QT	
Type	RPBA	**Size**	3/4"	
	Test History			
Test Date	7/29/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
Test Date	1/27/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	2

Serial #	A71920	**Test Due**	1/27/2012	
Location	Mechanical Room South Level1 - Makeup to heat pump			
Manufacturer	Watts	**Model**	009M3QT	
Type	RPBA	**Size**	3/4"	
	Test History			
Test Date	9/2/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
Test Date	1/27/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	2

Serial #	B22452	**Test Due**	1/27/2012	
Location	Pool Boiler Room - Pool makeup			
Manufacturer	Watts	**Model**	009M3QT	
Type	RPBA	**Size**	3/4"	
	Test History			
Test Date	9/2/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
Test Date	1/27/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	2

Serial #	A33975	**Test Due**	12/31/2011	
Location	Water entry room - Parkade hosebibs			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	2"	
	Test History			
Test Date	9/2/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
Test Date	12/31/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	2

Serial #	A33959	**Test Due**	12/31/2011	
Location	Water entry room - irrigation			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	2"	
	Test History			
Test Date	9/2/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	

Existing Backflow Prevention Assemblies
Town of Osoyoos

776.001	Watermark Resorts			HSC
Test Date	12/31/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
			Total Tests	2
Serial #	B22643	Test Due	1/27/2012	
Location	Mechanical room North end level 1 - Rest/park heat pump			
Manufacturer	Watts	Model	009M3QT	
Type	RPBA	Size	3/4"	
Test History				
Test Date	9/2/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	Tester #	7633	
Test Date	1/27/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
			Total Tests	2

Serial #	B22612	Test Due	1/27/2012	
Location	3rd Floor Mechanical room - makeup water			
Manufacturer	Watts	Model	009M3QT	
Type	RPBA	Size	3/4"	
Test History				
Test Date	9/2/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	Tester #	7633	
Test Date	1/27/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
			Total Tests	2

Serial #	B22476	Test Due	1/27/2012	
Location	5th Floor Mechanical room South - makeup water			
Manufacturer	Watts	Model	009M3QT	
Type	RPBA	Size	3/4"	
Test History				
Test Date	9/2/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	Tester #	7633	
Test Date	1/27/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
			Total Tests	2

Serial #	B22641	Test Due	2/22/2012	
Location	Poolside Pump room - pool auto fill			
Manufacturer	Watts	Model	009M3QT	
Type	RPBA	Size	3/4"	
Test History				
Test Date	9/2/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	Tester #	7633	
Test Date	2/22/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
			Total Tests	2

Serial #	B09476	Test Due	9/2/2010	
Location	Column of outdoor shower - outdoor shower			
Manufacturer	Watts	Model	007M3QT	
Type	DCVA	Size	3/4"	

776.001	Watermark Resorts			HSC
Test History				
Test Date	9/2/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
			Total Tests	1
Serial #	A19910	**Test Due**	12/31/2011	
Location	Fire system supply TH5			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
Test History				
Test Date	12/31/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	1

Serial #	A29601	**Test Due**	12/31/2011	
Location	Fire system supply TH4			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
Test History				
Test Date	12/31/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	01476	
			Total Tests	1

Serial #	A20896	**Test Due**	12/31/2011	
Location	Fire system supply TH 3			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
Test History				
Test Date	12/31/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	1

Serial #	A29595	**Test Due**	12/31/2011	
Location	Fire system supply TH 2			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
Test History				
Test Date	12/31/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	1

Serial #	A19924	**Test Due**	12/31/2011	
Location	Fire system supply TH 1			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
Test History				
Test Date	12/31/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	1

Existing Backflow Prevention Assemblies
Town of Osoyoos

776.001	Watermark Resorts			HSC
Serial #	A97478	**Test Due**	1/27/2012	
Location	Heat pump makeup			
Manufacturer	Watts	**Model**	009M3QT	
Type	RPBA	**Size**	3/4"	
Test History				
Test Date	1/27/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	1

Serial #	ID 605	**Test Due**	12/31/2011	
Location	Fire system supply			
Manufacturer	Ames	**Model**	200DC	
Type	DCVA	**Size**	4"	
Test History				
Test Date	12/31/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	1

Serial #	A57740	**Test Due**	1/27/2012	
Location	Tower makeup line			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	2"	
Test History				
Test Date	1/27/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	1

778.000	HOLDINGS LTD. (Super Value) (Family Foods)			HS
Serial #	21L1209	**Test Due**	11/30/2012	
Location	2) Fire system supply in utility room			
Manufacturer	Ammes	**Model**	2000SS	
Type	DCVA	**Size**	4 inch	
Test History				
Test Date	11/30/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Agnew	**Tester #**	5337	
Test Date	7/20/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Joshua Bonell	**Tester #**	8123	
Test Date	9/29/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	11/14/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	4

Serial #	266035	**Test Due**	11/14/2012	
Location	Mechanical room for fire protection			
Manufacturer	Watts	**Model**	009N2QTRP	
Type	RPBA	**Size**	2 inch	
Test History				
Test Date	7/20/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Joshua Bonell	**Tester #**	8123	
Test Date	9/29/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	11/14/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	3

Existing Backflow Prevention Assemblies
Town of Osoyoos

789.010	KOLE - Pioneer Carwash			HSC
Serial #	123952	**Test Due**	9/30/2012	
Location	In Mechanical Room			
Manufacturer	Watts	**Model**	009 M2 QT	
Type	RPBA	**Size**	1 1/2"	
Test History				
Test Date	6/11/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/24/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Heibig	**Tester #**	6614	
Test Date	9/30/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	3

804.000	OSOYOOS CREDIT UNION			MSC
Serial #	451774	**Test Due**	8/12/2012	
Location	Premise isolation in basement			
Manufacturer	Watts	**Model**	9 9M1QT	
Type	RPBA	**Size**	2"	
Test History				
Test Date	7/8/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Jeremy Davy	**Tester #**	7633	
Test Date	8/12/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Crag Johnson	**Tester #**	6995	
			Total Tests	2

815.000	BANK OF MONTREAL			LSC
Serial #	257523	**Test Due**	8/4/2012	
Location	Water Room/Storage			
Manufacturer	Apollo	**Model**	DCVA	
Type	DCVA	**Size**	1 1/2"	
Test History				
Test Date	8/4/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Chad Neufeld	**Tester #**	8439	
			Total Tests	1

842.000	LEE - Golden Chopsticks			MSC
Serial #	B08188	**Test Due**	10/28/2012	
Location	Premise isolation on main			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	1"	
Test History				
Test Date	10/28/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Wilchynski	**Tester #**	10478	
Test Date	10/2/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	**Tester #**	6085	
			Total Tests	2

Existing Backflow Prevention Assemblies
Town of Osoyoos

842.000	LEE - Golden Chopsticks			MSC
Serial #	336253	**Test Due**	10/28/2012	
Location	Ice maker isolation			
Manufacturer	Watts	**Model**	009QT	
Type	RPBA	**Size**	1/2"	
Test History				
Test Date	10/28/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Wilchynski	**Tester #**	10478	
Test Date	10/2/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	**Tester #**	6085	
			Total Tests	2

Serial #	345552	**Test Due**	10/28/2012	
Location	Cooler makeup line			
Manufacturer	Watts	**Model**	009QT	
Type	RPBA	**Size**	1/2"	
Test History				
Test Date	10/28/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Wilchynski	**Tester #**	10478	
Test Date	10/2/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	**Tester #**	6085	
			Total Tests	2

934.010	Osoyoos Elementary - Okanagan - Similkameen School District			MSC
Serial #	NM 264	Test Due	7/25/2012	
Location	Mechanical Room			
Manufacturer	Conbraco	Model	4DC0	
Type	DCVA	Size	4"	
Test History				
Test Date	5/2/2008	Test Result	☐ Failed	☑ Passed
Tester Name	Ben Johnson	Tester #	4345	
Test Date	8/18/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Brad Westen	Tester #	4364	
Test Date	8/26/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Brad Westen	Tester #	4364	
Test Date	7/25/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Bruce Porteous	Tester #	10475	
			Total Tests	4

934.020	SONORA COMMUNITY CENTRE			HSC
Serial #	FH-0295	Test Due	3/9/2012	
Location	Mechanical Room that serves the Fire Sprinklers			
Manufacturer	Watts	Model	757	
Type	DCVA	Size	4"	
Test History				
Test Date	2/14/2006	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	6/4/2007	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	3/23/2009	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	3/23/2010	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	7854	
Test Date	5/28/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	3/9/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	6

Serial #	178394	Test Due	3/9/2012	
Location	Basement mechanical room			
Manufacturer	Watts	Model	909	
Type	RPBA	Size	3 inch	
Test History				
Test Date	6/4/2007	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	3/23/2009	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	3/23/2010	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	7854	
Test Date	5/28/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	3/9/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	

934.020	SONORA COMMUNITY CENTRE			HSC
			Total Tests	5

965.000	OSOYOOS GOLF & COUNTRY			HSC
Serial #	113055	**Test Due**	5/10/2012	
Location	2) Fire system supply in mechanical room			
Manufacturer	Ames	**Model**	2000SS	
Type	DCVA	**Size**	4 inch	
	Test History			
Test Date	6/11/2004	**Test Result**	☑ Failed	☐ Passed
Tester Name	OK Fire Pro J.W.	**Tester #**		
Test Date	6/4/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	7/13/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	2/16/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	5/10/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	5

Serial #	93353	**Test Due**	5/10/2012	
Location	4) Irrigation system supply in mechanical room			
Manufacturer	Watts	**Model**	007M1 QT	
Type	DCVA	**Size**	2 inch	
	Test History			
Test Date	6/4/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	7/13/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	3/16/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	5/10/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	4

Serial #	35166	**Test Due**	5/10/2012	
Location	MECHANICAL ROOM			
Manufacturer	WATTS	**Model**	009M2QT	
Type	RPBA	**Size**	1 1/4"	
	Test History			
Test Date	2/15/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	VINCE CHAPMAN	**Tester #**	5306	
Test Date	6/4/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	7/13/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	2/16/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	5/10/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	5

965.000	OSOYOOS GOLF & COUNTRY			HSC
Serial #	124942	Test Due	5/10/2012	
Location	MECHANICAL ROOM			
Manufacturer	WATTS	Model	009M2QT	
Type	RPBA	Size	1 1/2"	
Test History				
Test Date	2/15/2006	Test Result	☐ Failed	☑ Passed
Tester Name	VINCE CHAPMAN	Tester #	5306	
Test Date	6/4/2007	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	7/13/2009	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	2/16/2010	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	5/10/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	5

965.000.010	Osoyoos Golf & Country Maintenance building			HSC
Serial #	274407	Test Due	5/10/2012	
Location	On main to sprayer			
Manufacturer	Watts	Model	009M2QT	
Type	RPBA	Size	2"	
Test History				
Test Date	5/12/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	5/10/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	2

Serial #	97838	Test Due	5/10/2012	
Location	Secondary spray filler			
Manufacturer	Watts	Model	009M2QT	
Type	RPBA	Size	1 1/2"	
Test History				
Test Date	7/13/2009	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	5/12/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	5/10/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	3

985.210	O.K. Center			HSC
Serial #	243493	**Test Due**	12/14/2012	
Location	Premise Isolation			
Manufacturer	Watts	**Model**	009M3QT	
Type	RPBA	**Size**	3/4"	
	Test History			
Test Date	12/14/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
Test Date	12/1/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	2

985.319	OKANAGAN KOOTENAY STERILE			HSC
Serial #	AC9438	**Test Due**	4/26/2012	
Location	3) Irrigation system supply in boiler room			
Manufacturer	Febco	**Model**	805Y	
Type	DCVA	**Size**	11/2 inch	
	Test History			
Test Date	10/1/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Gaien Bond	**Tester #**	7845	
Test Date	10/26/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	12/12/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	**Tester #**	5341	
Test Date	4/25/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	11/6/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	11/25/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	10/15/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	7

Serial #	22845	**Test Due**	10/26/2012	
Location	Domestic - boiler room			
Manufacturer	Watts	**Model**	009	
Type	RPBA	**Size**	3"	
	Test History			
Test Date	10/1/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Gaien Bond	**Tester #**	7845	
Test Date	10/26/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	12/12/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	**Tester #**	5341	
Test Date	3/1/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	J. Samuelson	**Tester #**	2452	
Test Date	12/8/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	11/6/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	

985.319	OKANAGAN KOOTENAY STERILE			HSC
Test Date	11/25/2008	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	10/15/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	8

Serial #	EL-1441	Test Due	10/26/2012
Location	Boiler room - fire protection		
Manufacturer	Watts	Model	757
Type	DCVA	Size	4"

Test History

Test Date	10/1/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Gaien Bond	Tester #	7845	
Test Date	10/26/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	12/12/2006	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	Tester #	5341	
Test Date	3/1/2005	Test Result	☐ Failed	☑ Passed
Tester Name	J. Samuelson	Tester #	2452	
Test Date	12/8/2005	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	11/6/2007	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	11/25/2008	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	10/15/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	8

Serial #	TV494	Test Due	10/26/2012
Location	Kettle Room		
Manufacturer	Conbraco	Model	40205T2
Type	RPBA	Size	1"

Test History

Test Date	10/1/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Gaien Bond	Tester #	7845	
Test Date	10/26/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	12/12/2006	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	Tester #	5341	
Test Date	5/31/2005	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	12/8/2005	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	11/6/2007	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	11/25/2008	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	10/15/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
			Total Tests	8

985.319	OKANAGAN KOOTENAY STERILE			HSC
Serial #	UQ865	**Test Due**	10/26/2012	
Location	Boiler Room			
Manufacturer	Conbraco	**Model**	40203T2	
Type	RPBA	**Size**	1/2	
	Test History			
Test Date	10/1/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	12/12/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Kellendonk	**Tester #**	5341	
Test Date	12/8/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	11/6/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	11/25/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	10/15/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	10/26/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	7

Serial #	2Y316	**Test Due**	10/26/2012	
Location	Fire sprinkler - Glycol mezzanine stairwell			
Manufacturer	Conbraco	**Model**	40208T2	
Type	RPBA	**Size**	2"	
	Test History			
Test Date	10/1/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	10/26/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	12/12/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	11/6/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	11/25/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	10/15/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	6

Serial #	X4637	**Test Due**	10/26/2012	
Location	Boiler Room - above boiler #2			
Manufacturer	Conbraco	**Model**	40207T2	
Type	RPBA	**Size**	1 1/2"	
	Test History			
Test Date	10/1/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	10/15/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	10/26/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	

Existing Backflow Prevention Assemblies
Town of Osoyoos

985.319	OKANAGAN KOOTENAY STERILE			HSC
			Total Tests	3

985.322	TOWN OF OSOYOOS - Public Works Shop			HSC
Serial #	RZ640	**Test Due**	7/18/2012	
Location	SOUTH SIDE OF GARAGE			
Manufacturer	COMBRACO	**Model**	40107T2	
Type	DCVA	**Size**	1 1/2"	
	Test History			
Test Date	3/6/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	4/22/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/18/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	4

Serial #	TK756	**Test Due**	7/18/2012	
Location	NORTH WEST CORNER OF GARAGE			
Manufacturer	COMBRACO	**Model**	40107T2	
Type	DCVA	**Size**	1 1/2"	
	Test History			
Test Date	3/6/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	4/22/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/18/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	4

Existing Backflow Prevention Assemblies
Town of Osoyoos

985.328	DARLORN CONSULTING & Septic Services			MSC
Serial #	48472	**Test Due**	5/27/2012	
Location	Zone - behind staircase in storage area			
Manufacturer	Watts	**Model**	007QT	
Type	DCVA	**Size**		
	Test History			
Test Date	2/14/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	Nick Hebig	**Tester #**	6177	
Test Date	4/18/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/31/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	4/21/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/27/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	6

Serial #	171116	**Test Due**	5/27/2012	
Location	Premises - in shop bathroom beside toliet			
Manufacturer	Watts	**Model**	009M3-QT	
Type	RPBA	**Size**	3/4	
	Test History			
Test Date	2/14/2005	**Test Result**	☐ Failed	☑ Passed
Tester Name	Nick Hebig	**Tester #**	6177	
Test Date	4/18/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/31/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	4/21/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/27/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	6

Existing Backflow Prevention Assemblies
Town of Osoyoos

985.334	WRIGHT (Wright Autobody)			MSC
Serial #	50790	Test Due	5/19/2012	
Location	Irrigation, in closet above softener			
Manufacturer	Watts	Model	007QT	
Type	DCVA	Size	1/2	
Test History				
Test Date	2/17/2005	Test Result	☐ Failed	☑ Passed
Tester Name	Nick Hebig	Tester #	6177	
Test Date	5/3/2006	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	6/8/2007	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	4/22/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	5/11/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	5/19/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
			Total Tests	6

Serial #	166547	Test Due	5/19/2012	
Location	Premises - closet above softener			
Manufacturer	Watts	Model	007 M3 QT	
Type	DCVA	Size	3/4	
Test History				
Test Date	5/3/2006	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	2/17/2005	Test Result	☐ Failed	☑ Passed
Tester Name	Nick Hebig	Tester #	6177	
Test Date	6/8/2007	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	4/22/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	5/11/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	5/19/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
			Total Tests	6

Existing Backflow Prevention Assemblies
Town of Osoyoos

985.345	TOWN OF OSOYOOS - Visitors Centre			HSC
Serial #	NAH97	**Test Due**	4/23/2011	
Location	Fire sprinkler system - basement mech room			
Manufacturer	Conbraco	**Model**	DC	
Type	DCVA	**Size**	3"	
Test History				
Test Date	2/14/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Bahn	**Tester #**	1827	
Test Date	4/20/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Eric Votol	**Tester #**	7793	
Test Date	4/23/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Robinson	**Tester #**	7795	
			Total Tests	3

Serial #	A25742	**Test Due**	3/25/2012	
Location	Irrigation - basement mech room			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	1"	
Test History				
Test Date	2/14/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	**Tester #**	1827	
Test Date	2/25/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Brad Helerman	**Tester #**	7792	
Test Date	4/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Robert Doherty	**Tester #**	6405	
Test Date	3/25/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
			Total Tests	4

Serial #	A09110	**Test Due**	3/25/2012	
Location	Domestic supply - basement mechanical room			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
Test History				
Test Date	2/14/2008	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	**Tester #**	1827	
Test Date	2/25/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Brad Helman	**Tester #**	7792	
Test Date	4/5/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Robert Doherty	**Tester #**	6405	
Test Date	3/25/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Lance Maveety	**Tester #**	5129	
			Total Tests	4

Existing Backflow Prevention Assemblies
Town of Osoyoos

985.366	SOUTH OK CONCRETE			HSC
Serial #	263300	**Test Due**	6/1/2012	
Location	In form plant bathroom			
Manufacturer	Watts	**Model**	009M2	
Type	RPBA	**Size**	2"	
	Test History			
Test Date	4/22/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	561	
Test Date	7/4/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	4/21/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	6/1/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	5

Serial #	A23087	**Test Due**	6/1/2012	
Location	In bathroom in office			
Manufacturer	Watts	**Model**	007M3QT	
Type	DCVA	**Size**	3/4	
	Test History			
Test Date	4/24/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/4/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	4/21/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	6/1/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	5

Serial #	123429	**Test Due**	6/1/2012	
Location	In Batch Plant			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1 1/2	
	Test History			
Test Date	7/4/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	4/21/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	6/1/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	4

986.050	MENDES - Desert Model Railroad			MSC
Serial #	DU586	**Test Due**	12/30/2012	
Location	2) Irrigation system supply in crawl space			
Manufacturer	Combraco	**Model**	4010599T	
Type	DCVA	**Size**	1 inch	
Test History				
Test Date	6/11/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	**Tester #**	6443	
Test Date	12/30/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	12/9/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	3

986.060	OGILVY			MSC
Serial #	290730	**Test Due**	10/31/2012	
Location	Mechanical room			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1"	
Test History				
Test Date	10/31/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	6/8/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	**Tester #**		
Test Date	10/15/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	3

Serial #	037092	**Test Due**	6/23/2007	
Location	In Electrical Room			
Manufacturer	WATTS	**Model**	052M009	
Type	RPBA	**Size**	1"	
Test History				
Test Date	6/23/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	1

Existing Backflow Prevention Assemblies
Town of Osoyoos

986.120	KELOWNA DISPLAY SERVIC ES - SHOW IN MOTION		HSC
Serial #	210424	**Test Due**	8/3/2012
Location	West Building Car Wash		
Manufacturer	WATTS	**Model**	007M3QTDC
Type	DCVA	**Size**	3/4"

Test History

Test Date	6/4/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	5/13/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	7/13/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	8/3/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	4

Serial #	A25722	**Test Due**	8/3/2012
Location	Warehouse East		
Manufacturer	WATTS	**Model**	007M1QT
Type	DCV	**Size**	1"

Test History

Test Date	6/4/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	5/13/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	7/13/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	8/3/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
			Total Tests	4

987.000	Akehurst & Giltrap Restoration Ltd			MSC
Serial #	187142	**Test Due**	6/3/2010	
Location	In Bathroom			
Manufacturer	Watts	**Model**	007M3	
Type	DCVA	**Size**	3/4"	
	Test History			
Test Date	6/3/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Action Plumbing	**Tester #**	8123	
			Total Tests	1

Agri001	Sekhon			HSC
Serial #	3116329	**Test Due**	8/16/2011	
Location	Far NW corner irrigation			
Manufacturer	Wilkins	**Model**	975XL	
Type	RPBA	**Size**	2"	
	Test History			
Test Date	5/19/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dave Rorie	**Tester #**	2081	
Test Date	8/16/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	David Rorie	**Tester #**	2081	
			Total Tests	2

Serial #	2655895	**Test Due**	5/19/2011	
Location	irrigation system			
Manufacturer	Wilkins	**Model**	972xl	
Type	RPBA	**Size**	2 inch	
	Test History			
Test Date	5/19/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dave Rorie	**Tester #**	2081	
			Total Tests	1

Agri002	Crespo		HSAGRI
Serial #	2355910	**Test Due**	6/24/2009
Location	irrigation system		
Manufacturer	Wilkins	**Model**	975xl
Type	RPBA	**Size**	2 inch

Agri003	Zandvliet		HSAGRI
Serial #	2655902	**Test Due**	5/19/2009
Location	irrigation system		
Manufacturer	Wilkins	**Model**	975xl
Type	RPBA	**Size**	2 inch

Agri004	Charanjit Kaur Dahliwal		HSC
Serial #	2672255	**Test Due**	5/19/2011
Location	irrigation system		
Manufacturer	Wilkins	**Model**	975xl
Type	RPBA	**Size**	2 inch

Existing Backflow Prevention Assemblies
Town of Osoyoos

Agri004	Charanjit Kaur Dahliwal			HSC
Test History				
Test Date	5/19/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Dave Rorie	Tester #	2081	
			Total Tests	1

Agri005	Sidhu Orchards			HSAGRI
Serial #	26559507	Test Due	7/28/2010	
Location	irrigation system			
Manufacturer	Wilkins	Model	975xl	
Type	RPBA	Size	2 inch	
Test History				
Test Date	7/28/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Fallowfield	Tester #	6443	
			Total Tests	1

Agri006	Monica Ondrus			HSAGRI
Serial #	2655905	Test Due	6/24/2009	
Location	irrigation system			
Manufacturer	Wilkins	Model	975xl	
Type	RPBA	Size	2 inch	

Agri010	Julius and Elda Horvath			HSAGRI
Serial #	2655901	Test Due	6/24/2009	
Location	irrigation system			
Manufacturer	Wilkins	Model	975xl	
Type	RPBA	Size	2 inch	

Agri011	Jennifer Dutra - Gaspar			HSC
Serial #	2672244	Test Due	7/20/2010	
Location	irrigation system			
Manufacturer	Wilkins	Model	975xl	
Type	RPBA	Size	2 inch	
Test History				
Test Date	7/20/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Mike Followfield	Tester #	6443	
			Total Tests	1

Agri017	Harg Sidhu			HSAGRI
Serial #	3237340XLTCU	Test Due	5/2/2012	
Location	Irrigation supply - mid property			
Manufacturer	Wilkins	Model	955XL	
Type	RPBA	Size	2"	
Test History				
Test Date	5/2/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Lance Soare	Tester #	2078	
			Total Tests	1

Existing Backflow Prevention Assemblies
Town of Osoyoos

Casa Del Lag	CASA DEL LAGO - Okanagan Strata Management			HSC
Serial #	NX723	**Test Due**	10/19/2012	
Location	Fire sprinkler - South parkade mech room			
Manufacturer	Conbraco	**Model**	4DC	
Type	DCVA	**Size**	4"	
Test History				
Test Date	8/20/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	**Tester #**	1827	
Test Date	9/16/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	**Tester #**	1827	
Test Date	10/19/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	mark Rout	**Tester #**	10476	
			Total Tests	3

Serial #	NT374	**Test Due**	10/19/2012	
Location	Fire Sprinkler - parkade mech room North			
Manufacturer	Conbraco	**Model**	4DC	
Type	DCVA	**Size**	4"	
Test History				
Test Date	8/20/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	**Tester #**	1827	
Test Date	9/16/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Kevin Rahn	**Tester #**	1827	
Test Date	10/19/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	3

Serial #	100025	**Test Due**	10/19/2012	
Location	North mechanical room			
Manufacturer	Watts	**Model**	009M2QT	
Type	RPBA	**Size**	1 1/2 inch	
Test History				
Test Date	6/8/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/13/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	
Test Date	7/13/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Galen Bond	**Tester #**	7845	
Test Date	10/19/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Mark Rout	**Tester #**	10476	
			Total Tests	4

Serial #	87504	**Test Due**	10/19/2012	
Location	Mechanical room in rec centre (Irrigation)			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2 inch	
Test History				
Test Date	6/8/2007	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/13/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	John Samuelson	**Tester #**	2452	

Existing Backflow Prevention Assemblies
Town of Osoyoos

Casa Del Lag	CASA DEL LAGO - Okanagan Strata Management			HSC
Test Date	7/13/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	10/19/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
			Total Tests	4

Serial #	187275	Test Due	10/19/2012
Location	POOL MECH ROOM (REC ROOM)		
Manufacturer	WATTS	Model	009
Type	RPBA	Size	3/4"

Test History

Test Date	5/18/2006	Test Result	☐ Failed	☑ Passed
Tester Name	SHAWN LAWLEY	Tester #	6085	
Test Date	7/13/2009	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	7/13/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	10/19/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
			Total Tests	4

Serial #	82400	Test Due	10/19/2012
Location	MECHANICAL ROOM - Irrigation		
Manufacturer	WATTS	Model	007M2QT
Type	DCVA	Size	1 1/2

Test History

Test Date	4/27/2006	Test Result	☐ Failed	☑ Passed
Tester Name	Shawn Lawley	Tester #	6085	
Test Date	6/8/2007	Test Result	☐ Failed	☑ Passed
Tester Name	Howard Hebig	Tester #	6614	
Test Date	7/13/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	10/19/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
			Total Tests	4

Serial #	XT365	Test Due	10/19/2012
Location	Pond Makeup		
Manufacturer	Conbraco	Model	40204T2
Type	RPBA	Size	3/4"

Test History

Test Date	7/13/2009	Test Result	☐ Failed	☑ Passed
Tester Name	John Samuelson	Tester #	2452	
Test Date	7/13/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Galen Bond	Tester #	7845	
Test Date	10/19/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Mark Rout	Tester #	10476	
			Total Tests	3

Existing Backflow Prevention Assemblies
Town of Osoyoos

CDMOR001	Casa Del Mila Oro Resort & Spa			HSC
Serial #	326985	**Test Due**	12/30/2012	
Location	Pool makeup supply			
Manufacturer	Watts	**Model**	009M3QT	
Type	RPBA	**Size**	3/4"	
Test History				
Test Date	12/30/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Chad Neufeld	**Tester #**	8439	
			Total Tests	1

Serial #	XP648	**Test Due**	10/1/2011	
Location	Irrigation system supply			
Manufacturer	Conbraco	**Model**	40108T2	
Type	DCVA	**Size**	2"	
Test History				
Test Date	10/1/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Chad Neufeld	**Tester #**	8439	
			Total Tests	1

Serial #	11475	**Test Due**	10/12/2011	
Location	Fire system supply - NOT LOCATED			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	1 1/2"	
Test History				
Test Date	10/12/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Test Clear	**Tester #**		
			Total Tests	1

Serial #	A1233567	**Test Due**	10/12/2011	
Location	Domestic supply in crawlspace - NOT LOCATED			
Manufacturer	Watts	**Model**	007M3QT	
Type	DCVA	**Size**	3/4"	
Test History				
Test Date	10/12/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Test Clear	**Tester #**		
			Total Tests	1

Serial #	A38804	**Test Due**	10/24/2012	
Location	Geothermal Isolation			
Manufacturer	Watts	**Model**	007M3QT	
Type	DCVA	**Size**	3/4"	
Test History				
Test Date	10/1/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Chad Newfeld	**Tester #**	8439	
Test Date	10/24/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Chad Newfeld	**Tester #**	8439	
			Total Tests	2

Existing Backflow Prevention Assemblies
Town of Osoyoos

CF001	Cactus Flats - Strata Pro			HSC
Serial #	11689	Test Due	10/24/2012	
Location	Sprinkler room premise isolation			
Manufacturer	Watts	Model	007DC	
Type	DCVA	Size	3"	
Test History				
Test Date	5/31/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Firestone Mechanical	Tester #	8120	
Test Date	7/20/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Wyatt Reogh	Tester #	10188	
Test Date	10/24/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Chad Newfeld	Tester #	8439	
			Total Tests	3

Serial #	154091	Test Due	10/24/2012	
Location	Fire system supply			
Manufacturer	Conbraco	Model	40108T2	
Type	DCVA	Size	2"	
Test History				
Test Date	5/31/2009	Test Result	☐ Failed	☑ Passed
Tester Name	G & G	Tester #	7235	
Test Date	7/20/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Wyatt Keogh	Tester #	10188	
Test Date	10/24/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Chad Newfeld	Tester #	8439	
			Total Tests	3

Serial #	A34843	Test Due	10/24/2012	
Location	Irrigation system connection			
Manufacturer	Watts	Model	009M2QT	
Type	RPBA	Size	1 1/2"	
Test History				
Test Date	5/31/2009	Test Result	☐ Failed	☑ Passed
Tester Name	Firestone Mechanical	Tester #	8120	
Test Date	7/20/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Wyatt Keogh	Tester #	10188	
Test Date	10/24/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Chad Newfeld	Tester #	8439	
			Total Tests	3

Existing Backflow Prevention Assemblies
Town of Osoyoos

CR001	Cactus Ridge			HSC
Serial #	187845	**Test Due**	2/3/2012	
Location	Mechanical room premise isolation			
Manufacturer	Watts	**Model**	709	
Type	DCVA	**Size**	4"	
Test History				
Test Date	1/4/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Firestone Mech	**Tester #**	8120	
Test Date	2/3/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	2

Serial #	IJ-0061	**Test Due**	2/3/2012	
Location	Fire system supply			
Manufacturer	Watts	**Model**	757	
Type	DCVA	**Size**	4"	
Test History				
Test Date	1/4/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Firestone	**Tester #**	8120	
Test Date	2/3/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	2

Serial #	A42469	**Test Due**	2/3/2012	
Location	Irrigation system supply			
Manufacturer	Watts	**Model**	007M2QT	
Type	DCVA	**Size**	2"	
Test History				
Test Date	2/3/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	1

Existing Backflow Prevention Assemblies
Town of Osoyoos

INTS0001	Interior Savings			MSC
Serial #	A19180	Test Due	4/12/2012	
Location	Janitors room premise iso			
Manufacturer	Watts	Model	007M1QT	
Type	DCVA	Size	1"	
Test History				
Test Date	4/12/2011	Test Result	☐ Failed	☑ Passed
Tester Name	David Rorie	Tester #	2081	
			Total Tests	1

OBC001	Osoyoos Border Crossing			HSC
Serial #	114469	Test Due	10/19/2012	
Location	Public Washroom / Utility Room			
Manufacturer	Watts	Model	007M1QT	
Type	DCVA	Size	2"	
Test History				
Test Date	10/19/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Dale Grimes	Tester #	3632	
Test Date	11/22/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Craig Johnson	Tester #	6995	
			Total Tests	2

Serial #	41509	Test Due	10/19/2012	
Location	Admin Buidling 2nd Floor Boiler room			
Manufacturer	Febco	Model	825Y	
Type	RPBA	Size	3/4"	
Test History				
Test Date	10/19/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Dale Grimes	Tester #	3632	
Test Date	11/22/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Craig Johnson	Tester #	6995	
			Total Tests	2

Serial #	203304	Test Due	10/19/2012	
Location	Upstairs Mechanical room / De-Vaning			
Manufacturer	Watts	Model	009M2QT	
Type	RPBA	Size	1"	
Test History				
Test Date	10/19/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Dale Grimes	Tester #	3632	
Test Date	11/22/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Craig Johnson	Tester #	6995	
			Total Tests	2

Serial #	115633	Test Due	10/19/2012	
Location	Janitor room Admin 1st Floor			
Manufacturer	Watts	Model	007M1QT	
Type	DCVA	Size	2"	
Test History				
Test Date	10/19/2011	Test Result	☐ Failed	☑ Passed
Tester Name	Dale Grimes	Tester #	3632	
Test Date	11/22/2010	Test Result	☐ Failed	☑ Passed
Tester Name	Craig Johnson	Tester #	6995	

Existing Backflow Prevention Assemblies
Town of Osoyoos

OBC001	Osoyoos Border Crossing			HSC
			Total Tests	2
Serial #	122300	**Test Due**	10/19/2012	
Location	De-vaning Janitors room downstairs			
Manufacturer	Watts	**Model**	007M1QT	
Type	DCVA	**Size**	2"	
	Test History			
Test Date	10/19/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dale Grimes	**Tester #**	3632	
Test Date	11/22/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Craig Johnson	**Tester #**	6995	
			Total Tests	2

Serial #	H41511	**Test Due**	10/19/2012	
Location	Humidufier makeup line			
Manufacturer	Febco	**Model**	825Y	
Type	RPBA	**Size**	3/4"	
	Test History			
Test Date	10/19/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dale Grimes	**Tester #**	3632	
			Total Tests	1

Serial #	114437	**Test Due**	10/19/2012	
Location	Irrigtation system - vault by public washrooms			
Manufacturer	Watts	**Model**	007M!	
Type	DCVA	**Size**	2"	
	Test History			
Test Date	10/19/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Dale Grimes	**Tester #**	3632	
			Total Tests	1

TOO-1 WWTP	Town of Osoyoos - Lagoon waste water plant			HSC
Serial #	QV595	**Test Due**	7/18/2012	
Location	3) 2nd Main water supply enters in chlorine room as 1 inch			
Manufacturer	Combraco	**Model**	4020599T	
Type	RPBA	**Size**	1 inch	
	Test History			
Test Date	11/12/2002	**Test Result**	☑ Failed	☐ Passed
Tester Name		**Tester #**		
Test Date	11/12/2002	**Test Result**	☑ Failed	☐ Passed
Tester Name		**Tester #**		
Test Date	1/11/2006	**Test Result**	☐ Failed	☑ Passed
Tester Name	VINCE CHAPMAN	**Tester #**	5306	
Test Date	4/23/2009	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	5/11/2010	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
Test Date	7/18/2011	**Test Result**	☐ Failed	☑ Passed
Tester Name	Howard Hebig	**Tester #**	6614	
			Total Tests	6

Client Accounts List
Town of Osoyoos

PC	Account	Facility Name	Facility Address
AGNS	1177.010	FERREIRA	6401 TAMARACK DR
AGNS	1178.000	FARINHA	6808 45 STREET
AGNS	1179.010	SALMIC	7028 45 STREET
AGNS	1179.020	DE SOUSA	7024 45 STREET
AGNS	1256.020	WALTON	4107 36 AVENUE
AGNS	1316.005	GIL	6015 LAKESHORE
AGNS	1316.010	REZKA	6005 LAKESHORE
AGNS	1316.040	GRANT	5822 51 ST
AGNS	1316.045	GRANT	5816 51 ST
AGNS	1326.001	VIRK	4413 LAKESHORE
AGNS	1326.010	VIRK	44TH AVE
AGNS	1326.015	VIRK	44TH AVE
AGNS	1327.005	VIRK	LAKESHORE DR
AGNS	1332.005	BENZ	3013 LAKESHORE
AGNS	139.000	GOWING	6006 MAPLE DR
AGNS	304.050	RIZNEK	6015 MAPLE DRIVE
AGNS	307.000	LETHEBE	6313 JACKPINE LANE
AGNS	308.000	LETHEBE	6311 JACKPINE LANE
AGNS	309.000	FOUTY	6309 JACKPINE LANE
AGNS	310.000	MASSE	6307 JACKPINE LANE
AGNS	311.000	DOWIN	6305 JACKPINE LANE
AGNS	312.000	OGILVY	6303 JACKPINE LANE
AGNS	345.140	GABELMANN	10701 HWY # 3
AGNS	345.160	COSENS	8606 MEADOWLARK
AGNS	345.180	BUTTAR	10508 74 AVE
AGNS	345.220	MACIEL	8601 MEADOWLARK
AGNS	345.250	DEOL	7601 MEADOWLARK
AGNS	345.260	FARINHA	10120 74 AVENUE
AGNS	47.000	SILKE	6701 PONDEROSA DR
AGNS	48.000	SILKE	6703 PONDEROSA DR
AGNS	49.000	LIEBEL	6705 PONDEROSA DR
AGNS	50.000	PAVLOVIC	6707 PONDEROSA DR
AGNS	51.000	BASHOVSKI	6709 PONDEROSA DR
AGNS	52.000	HANCOCK	6901 PONDEROSA DR
AGNS	53.005	HAMPAUL, PAUL	6903 PONDEROSA DR
AGNS	53.010	HAMPAUL, PAUL	6905 PONDEROSA DR
AGNS	535.050	ROHLOFF	9901 74 AVE
AGNS	535.060	FERNANDES	7002 87 ST
AGNS	535.115	BABICH	10125 74 AVE
AGNS	535.120	JONES	10115 74 AVE
AGNS	535.140	SLATER	10105 74 AVE
AGNS	535.150	ARTUSO	9915 74 AVE
AGNS	535.160	MOREIRA	10129 74 AVE
AGNS	535.205	PFINGSTTAG	6216 97 STREET
AGNS	535.210	KRYGSVELD	6214 97 STREET
AGNS	535.230	KLYPAK	10110 62 AVE
AGNS	535.410	BENNETT	6814 MEADOWLARK
AGNS	535.420	BHANDOL	6218 97 ST
AGNS	535.475	ROQUE	10506 62 AVE

Client Accounts List
Town of Osoyoos

PC	Account	Facility Name	Facility Address
AGNS	54.005	HAMPAUL, PAUL	6907 PONDEROSA DR
AGNS	56.000	TOTH	6908 PONDEROSA DR
AGNS	577.030	KOROPATNICKI	19 MAGNOLIA PL
AGNS	59.000	DODD	6902 PONDEROSA DR
AGNS	60.000	NIELSEN	6708 PONDEROSA DR
AGNS	61.000	EHLERS	6706 PONDEROSA
AGNS	647.000	SLINGSBY	8704 74 AVE
AGNS	649.000	TOMLIN	8708 74 AVE
AGNS	650.000	OSLAND	8710 74 AVE
AGNS	651.000	CAPENEATA	8712 74 AVE
AGNS	652.000	ALIZADEH	7401 89 ST
AGNS	653.000	GAERTNER	8702 MAIN
AGNS	655.000	STRILKIWSKY	8710 MAIN
AGNS	658.000	BALOGH	8716 MAIN
AGNS	660.000	GECSE	8711 MAIN ST
AGNS	661.000	CUPELLO	8709 MAIN ST
AGNS	662.000	LABOUNTY	8707 MAIN ST
AGNS	67.000	PRIMEAU	7710 MAIN ST
AGNS	69.000	GOODWIN	6910 PONDEROSA DR
AGNS	714 06249.010	LLoyd Sauder	Block 598
AGNS	770.000	YUSEP	7609 SPARTAN
AGNS	78.000	RACZ	7502 MAIN ST
AGNS	792.000	SLATER	8323 MAIN ST
H	75.200	NICHOLSON HOLDINGS LTD. - Napili Shores	# 20-7308 MAIN
H	984.000	AGRI-PAK PACKAGING LTD	10401 115TH ST
H	985.306	Blair and Blake Ogilvy	10601 115th Street
H	986.010	Desert Storage Ltd	11636 115TH ST
H	SV001	Sole Vita	7200 Cottonwood Drive
HS	1000.140	Osoyoos Secondary School	5800 115th Street
HS	1316.035	BORDERTOWN SERVICE LTD.	6004 51 ST
HS	1324.020	Osoyoos RV & Waterslide	5003 LAKESHORE
HS	321.100	Rattle Snake Canyon	5502 Main St
HS	336.370	625131 BC Ltd- Okanagan RV Centre	6010 LAKESHORE DR
HS	336.400	ADRIATIC MOTEL INC.	5501 MAIN ST
HS	397120	Lakeview Plaza - c/o Record Financial	9150 Main Street
HS	515.000	Sun Bowl Arena	
HS	6027.000	Sandhu Green Houses - Harjeewa / Jasvir Sandhu	9707 - 128th Ave
HS	6065.020	Country Squire Villa	9705 87 Street
HS	769.005	Breeze Bar and Grill	7603 SPARTAN
HS	778.000	HOLDINGS LTD. (Super Value) (Family Foods)	8130 MAIN ST
HS	783.001	BEST-WAY BUILDERS CENTRE - Strip Mall	8111 MAIN ST
HS	825.000	BERGSTAD - Osooyoos Dental Centre	8524 MAIN ST
HS	826.001	OSOYOOS FOODS LTD. - Wildfire Grill	8526 MAIN ST
HS	885.000	Gurpiar and Gurdeep Aulakah	8301 72Ave - 8129 Main St
HS	985.324	EXTRACT MINERALS	11200 115TH ST
HS	985.340	Osoyoos Ready Mix / Osoyoos Aggregate	11648 115TH ST
HS	TOO-2 Pumpho	Town of Osoyoos - No. 6 Pump house	
HSAG	714.06262.000	Gurpiar Aulakh and Roop Sing Smagh	Block 608 - 2202 Hwy 97
HSAG	Agri002	Crespo	Block 578

Client Accounts List
Town of Osoyoos

PC	Account	Facility Name	Facility Address
HSAG	Agri003	Zandvliet	Block 577
HSAG	Agri005	Sidhu Orchards	Block 582 - 1220 107th Street
HSAG	Agri006	Monica Ondrus	Block 583
HSAG	Agri007	Leyden	Block 611
HSAG	Agri008	Leyden	Block 632
HSAG	Agri009	Unknown	Block 564
HSAG	Agri010	Julius and Elda Horvath	Block 600
HSAG	Agri012	Gomes	Block 609
HSAG	Agri015	Sekhon	Block 494
HSAG	Agri016	Sandhu	Block 470
HSAG	Agri017	Harg Sidhu	3201 107 Street
HSC	114.125	Palms By The Lake	6809 Cottonwood Drive
HSC	1256.010	Waltons Mountain Resort	3207 Lakeshore Drive
HSC	1323.000	Island View RV	5005 Lakeshore Drive
HSC	1326.000	Village on the Lake	4413 Lakeshore Drive
HSC	1334.010a	OASIS R.V. PARK LTD.	2615 LAKESHORE
HSC	1348.102	Las Ventanas	2418 Lakeshore
HSC	1353.012	Walnut Beach Resort	4200 Lakeshore Drive
HSC	138.010	DESIGN BURGER & DOGS INC. (Sage Pub)	6403 COTTONWOOD
HSC	290.010	550524 BC LTD. (Cottonwood Plaza)	6511 MAIN ST
HSC	314.000	SALIN HOLDINGS INC. (Dairy Queen)	5914 MAIN ST
HSC	321.200	551996 BC LTD (BEST WESTERN)	5506 MAIN ST
HSC	338.005	SAFARI BEACH RESORT LTD.	5815 OLEANDER DR
HSC	345.105	HUSKY OIL OPERATIONS LTD.	9206 97 STREET
HSC	345.163	FODEY	8214 MEADOWLARK
HSC	345.400	Mariposa Gardens - Baltic Properties Ltd.	8816 - 97 street
HSC	347.010	Buy Low Foods	9141 Main Street
HSC	347.210	MP Hospitality Ltd (Ridge Pub / Westridge Motor	9913 HIGHWAY # 3
HSC	348.025	509888 BC LTD. (A & W)	#7 EAGLE COURT
HSC	348.075	MCDONALD'S RESTAURANTS OF	#8 EAGLE COURT
HSC	398.010	Osoyoos Super 8	9130 Main Street
HSC	535.112	RICHTER - NAPA Phonix Auto Parts	7214 97 ST
HSC	535.250	TEJAY	10307 74 AVE
HSC	575.000	La Mirada	5003 Oleander Drive
HSC	6019.010	Okanagan Tree Fruit Coop - Monashee Packing Ho	87th Street Osoyoos
HSC	6078.010	DEOL BROS. FARMS LTD. (Shell)	9121 92 AVENUE
HSC	638.000	HOWARD'S SERVICE LTD	9101 MAIN ST
HSC	64.000	DESERT PROPERTIES LTD (Coast Hotel)	7702 MAIN ST
HSC	641.010	INTERIOR PROJECTS INC (Smitty's)	8906 MAIN ST
HSC	645.000	TOWN OF OSOYOOS (TOWN HALL) / Fire Hal	8707 MAIN ST
HSC	656.000	OSOYOOS TIMES LTD	8712 MAIN
HSC	657.000	PENDERGRAFT PROFESSIONAL	8714 MAIN
HSC	68.000	THE OWNERS (Holiday Inn)	7906 MAIN ST
HSC	71.000	SAIRAM HOLDINGS LTD. - Spanish Fiesta Reso	7104 MAIN
HSC	714.6265.000	Layden Vineyards	1230 Hwy 97
HSC	72.000	GOODLAD HOLDINGS LTD - Falcon Motel	7106 MAIN
HSC	772.016	White Sands Strata Corp - KAS1462	7803 Spartan Dr
HSC	776.001	Watermark Resorts	
HSC	789.010	KOLE - Pioneer Carwash	8310 74TH

Client Accounts List
Town of Osoyoos

PC	Account	Facility Name	Facility Address
HSC	934.020	SONORA COMMUNITY CENTRE	8505 68 AVE
HSC	965.000	OSOYOOS GOLF & COUNTRY	12300 Golf Course Drive
HSC	965.000.010	Osoyoos Golf & Country Maintenance building	
HSC	985.210	O.K. Center	9450 115TH ST
HSC	985.319	OKANAGAN KOOTENAY STERILE	11401 115TH ST
HSC	985.322	TOWN OF OSOYOOS - Public Works Shop	11500 115TH ST
HSC	985.345	TOWN OF OSOYOOS - Visitors Centre	9912 Hwy 3
HSC	985.366	SOUTH OK CONCRETE	11602 115TH ST
HSC	985.385	SOUTH OK CONCRETE	11624 115TH ST
HSC	986.120	KELOWNA DISPLAY SERVIC ES - SHOW IN	11625 115TH ST
HSC	Agri001	Sekhon	Block 571
HSC	Agri004	Charanjit Kaur Dahliwal	Block 578
HSC	Agri011	Jennifer Dutra - Gaspar	3626 Hwy 97 - Block 601
HSC	Casa Del Lago	CASA DEL LAGO - Okanagan Strata Management	7600 COTTONWOOD DRIVE
HSC	CDMOR001	Casa Del Mila Oro Resort & Spa	5401 Lakeshore
HSC	CF001	Cactus Flats - Strata Pro	5803 Lakeshore
HSC	CR001	Cactus Ridge	9107 Main Street
HSC	OBC001	Osoyoos Border Crossing	202 97th Street
HSC	TOO-1 WWTP	Town of Osoyoos - Lagoon waste water plant	62 AVE
L	1281.000	OSOYOOS INDIAN BAND	4702 MAIN ST
L	1319.000	PEMBOROUGH DEVELOPMENTS	4937 MAIN ST
L	320.000	Ken Crahart	5702 MAIN ST
L	38.000	OSOYOOS PYRAMID CORPOR	6901 MAIN ST
L	397.120	337669 B C LTD	9150 MAIN ST
L	644.000	TOWN OF OSOYOOS - Lease property	8713 MAIN ST
L	644.900	TOWN OF OSOYOOS - Development Services Bu	8711 MAIN ST
L	648.000	Elisabeth Pazdzidrski - Cougar Mountain Therapy	8706 74 AVE
L	786.020	GAERTNER HOLDINGS LTD	8149 MAIN ST
L	796.000	518196 BC LTD.	8315 MAIN ST
L	797.000	GAERTNER HOLDINGS LTD - Radio Shack	8313 MAIN
L	816.000	NUNES - Stedmans	8506 MAIN ST
L	833.000	PRAIRIE SCHOONER	7802 85TH ST
L	856.000	FOR-MAR HOLDINGS LTD - Pokadot Doors Flo	8141 MAIN ST
L	861.000	CAROLANN ENTERPRISES INC	8308 72 AVE
L	864.000	0837716 BC Ltd - 3D Moving and Storage	8307 74 AVE
L	891.000	Cascade Stucco Ltd - Desert Sun Councilling	8307 72 AVE
LS	1.000	KOBAIR HOLDINGS LTD. - BC Liquor Store	8110 MAIN ST
LS	1316.050	PEMBOROUGH DEVELOPMENTS -vacant lot	5601 LAKESHORE
LS	348.050	EDMAR HOLDINGS LTD (LORDCO)	10 EAGLE COURT
LS	36.000	PATEL - Queen Boutique	3 HARBOUR KEY DR
LS	771.000	CANTER HOLDINGS LTD - Stirp Mall	7611 SPARTAN
LS	786.030	BEST-WAY BUILDERS CENTRE - OK Tire	8147 MAIN ST
LS	791.000	Lori Baker - MLA Building	8312 74TH
LS	798.010	BEST-WAY BUILDERS CENTRE - Shoppers	8305 MAIN ST
LS	801.000	BUTULA - Lunatico Shop	8306 MAIN ST
LS	802.000	PAGEDENE HOLDINGS LTD - Eisenhut insurace	8308 MAIN ST
LS	807.000	SVEDRUZIC	8318 MAIN ST
LS	808.000	WONG - Unity Clothing	8320 MAIN ST
LS	809.000	BUTULA - Kick Start Printing	8322 MAIN

Client Accounts List
Town of Osoyoos

PC	Account	Facility Name	Facility Address
LS	810.000	FRASER REAL ESTATE AGENTS	8324 MAIN
LS	818.000	W D HLDG INC - Imperial Office	8510 MAIN ST
LS	819.000	DESERT OASIS REALTY LT	8512 MAIN ST
LS	820.050	CIBC DEVELOPMENT CORP	8516 MAIN ST
LS	822.000	MILLER - Thrift Store	8518 MAIN ST
LS	824.000	GONZALEZ - Lakeside Travel	8522 MAIN ST
LS	843.000	LEE - Desert Oasis Fashion	8523 MAIN
LS	844.000	LEE - Into Hair & Body	8521 MAIN
LS	845.000	DEBOER - Your Movie Store	8519 MAIN
LS	847.000	HAMMERSLEY - First Choice Health Foods	8511 MAIN
LS	848.000	FISCHER - Rudys Flooring	8509 MAIN
LS	849.000	ROB DALE HOLDINGS LTD. - Remax	8507 MAIN
LS	850.000	CARLAR ENTERPRISES LTD - Home Hardware	8501 MAIN
LS	923.000	Caleb Industries Inc - Flowers on Main	8317 MAIN ST
LSC	1316.015	B A T INDUSTRIES LTD	6001 LAKESHORE
LSC	1316.020	486111 B C LTD	5813 LAKESHORE
LSC	623.000	SOUTHERN OKANAGAN - Double O Bikes	8905 MAIN ST
LSC	646.000	TOWN OF OSOYOOS (Interior Health)	8701 MAIN ST
LSC	663.010	GAERTNER HOLDINGS LTD	8705 78 AVE
LSC	664.000	GAERTNER HOLDINGS LTD	8703 78 AVE
LSC	786.010	BEST-WAY BUILDERS CENTRE	8304 74TH AVE
LSC	788.000	TOWN OF OSOYOOS	8306 74TH
LSC	811.000	TOWN OF OSOYOOS	8313 78 AVE
LSC	815.000	BANK OF MONTREAL	8502 MAIN ST
LSC	834.000	TOWN OF OSOYOOS	8502 74 AVE
LSC	892.000	PALMATEER	8305 72 AVE
M	290.110	THE DESERT MIRAGE	15 SOLANA KEY CRT
M	345.275	Peters Cafe	7414 Hwy 97 South
M	556.000	494888 BC LTD. (LAKEVIEW GROCERY)	5820 89 STREET
M	573.745	Greycon Homes Ltd	4809 89 St
M	620.000	DIAMOND STEAK & SEAFOOD	8901 MAIN ST
M	714.6330.000	BUCK, DAVID	1812 89TH STREET
M	79.000	RICHTER PASS MOTOR INN	7504 MAIN ST
M	793.010	ANDERSON	8319 MAIN ST
M	812.000	M & E VENTURES LTD. - Hong Kong Restraunt	8311 78 AVE
M	813.000	M & E VENTURES LTD.	8307 78 AVE
M	830.000	AULAKH	8507 78 AVE
M	831.000	COLLINS	8505 78 AVE
M	832.000	MARRIOTT	8503 78 AVE
M	836.000	MORRIS	8506 74 AVE
M	837.000	MCNEIL	8508 74 AVE
M	838.000	WEST	8510 74 AVE
M	840.010	PRESIDENT OF THE LETHB - Church of Latterd	8514 74 AVE
M	853.000	AMANAT	8133 MAIN
M	854.100	AMANAT	8135 MAIN
M	854.500	AMANAT	8137 MAIN
M	855.000	REINHOLD	8139 MAIN ST
M	857.000	NICOLINAS	8143 MAIN ST
M	858.000	CHAVES	8145 MAIN ST

Client Accounts List
Town of Osoyoos

PC	*Account*	*Facility Name*	*Facility Address*
M	859.000	PEARCE	8304 72 AVE
M	860.000	KROENKE	8306 72 AVE
M	862.000	BIRKLAND	8310 72 AVE
M	863.000	DOMENE	8309 74 AVE
M	865.000	WELLMAN	8305 74 AVE
M	866.000	ANDERSON	8303 74 AVE
M	874.000	ROTH	8513 74 AVE
M	875.000	LIPPA	8511 74 AVE
M	876.000	MERCHANT	8509 74 AVE
M	877.000	GRUHL	8507 74 AVE
M	878.000	STEA	8505 74 AVE
M	879.000	GIBBINS	8503 74 AVE
M	880.000	HEYDUCK	7204 85 ST
M	881.010	SANAI	8115 MAIN ST
M	883.000	GILL	8121-8125 MAIN ST
M	884.000	REINHOLD	8127 MAIN
M	886.010	DELUCA	8304 70 AVE
M	887.000	DELUCA	8306 70 AVE
M	888.000	CROWLEY	8308 70 AVE
M	889.000	BARICHKA	8310 70 AVE
M	890.000	DALLAS	7003 85 ST
M	893.000	ORLOWSKI	8303 72 AVE
M	921.000	KOBAIR HOLDINGS LTD.	8108 MAIN ST
M	923.050	ZELKO	8315 68 AVE
M	923.100	ORLOWSKI	8313 68 AVE
M	925.000	ASSELIN	8311 68 AVE
M	926.000	SCHLEPPE	8309 68 AVE
M	927.000	TEMPLE	8305 68 AVE
M	928.000	WILLSON	8303 68 AVE
M	984.010	HAMMERLE	10201 115TH ST
M	985.220	VIEIRA	N/A
M	985.280	USHER	10200 115TH ST
M	985.302	STORWICK	10001 115TH ST
M	985.308	OKANAGAN Tree Fruit Coop	10801 115TH ST
M	985.310	LOURA	10901 115TH ST N/A
M	985.311	ERDELJAC	N/A
M	985.313	MOLENKAMP	11001 115TH ST
M	985.316	BRUGMAN	11201 115TH ST
M	985.317	NEILSON	N/A
M	985.326	LEHMAN	11110 115TH ST
M	985.330	NEILSON	11100 115TH ST
M	985.332!	NEILSON	N/A
M	985.336	WRIGHT	N/A
M	985.390	SMITH	11601 115TH ST
M	986.000	TARRANT	11634 115TH ST
M	986.070	HEPPELL	11615 115TH ST
M	986.080	LEES	11617 115TH ST N/A
M	987.050	TARRANT	11630 115TH ST
M	987.060	TARRANT	11632 115TH ST

Client Accounts List
Town of Osoyoos

PC	*Account*	*Facility Name*	*Facility Address*
M	DS0001	Dollar Store Building	
MS	1316.030	HOFFMAN Motors	6014 51 ST
MS	305.000	JUNG (Sahara Courtyard Inn)	6205 COTTONWOOD DR
MS	553.500	G.P.A. Property Management - Osoyoos Lakeview	6002 89 STREET
MS	577.020	Destiny Beach Resort	20 MAGNOLIA PL
MS	74.000	Mimos Investments Ltd - Green Gables Resort	7304 MAIN
MS	800.000	D & J Osoyoos Holdings Ltd	8302 MAIN ST
MS	814.020	M & E VENTURES LTD. - Pharmasave	8301 78 AVE
MS	846.000	Mohammed Sobhani & Shahla Nikanpour - Mamis	8515 MAIN
MS	985.290	Cidalia & Gina Harpman	11500 STRAWBERRY CREEK RD
MS	TOO-9 Pumpho	No. 9 Pump House	ACIACA
MSC	138.000	HUDSON (Riviera Motel)	6004 MAPLE DR
MSC	348.015	CANTER HOLDINGS LTD - 711 Store	11 Eagle Court
MSC	348.150	RCMP	16 Eagle Court
MSC	443.000	Osoyoos Nursery School	6609 89th St
MSC	535.220	ELKS (OSOYOOS) LODGE NO 436 B P	6210 97 STREET
MSC	55.005	Ambrosia Restraunt	6910 MAIN STREET
MSC	573.340	Interior Health (Sagebrush Lodge)	4816 89th St
MSC	58.000	MANDZIUK HOTELS LTD (Bella Villa Motel)	6904 PONDERSOA DR
MSC	62.000	HUDSON (Poplars Motel)	6404 COTTONWOOD
MSC	624.010	Tim Hortons	8907 Main Street
MSC	758.000	CALDER (Osoyoos Medical Clinic)	7802 SPARTAN
MSC	77.000	Desert Surfside	7310 MAIN ST
MSC	804.000	OSOYOOS CREDIT UNION	8310 MAIN ST
MSC	806.000	MEL MAXWELL ENTERPRISES	8316 MAIN ST
MSC	842.000	LEE - Golden Chopsticks	8527 MAIN
MSC	852.000	462720 B.C. LTD. (Wine Kitz)	8131 MAIN
MSC	934.010	Osoyoos Elementary - Okanagan - Similkameen Sc	8507 - 68th Avenue
MSC	985.328	DARLORN CONSULTING & Septic Services	11106 115TH ST
MSC	985.334	WRIGHT (Wright Autobody)	10900 115ST
MSC	986.025	FORT STORAGE - RON BRADY	11640 115TH ST
MSC	986.040	SHIELDS	11642 115TH ST
MSC	986.050	MENDES - Desert Model Railroad	11611 115TH ST
MSC	986.060	OGILVY	11613 115TH ST
MSC	986.090	LEES	11619 115TH ST
MSC	986.105	MORESBY FUELS LTD	11621-11623 115TH ST
MSC	987.000	Akehurst & Giltrap Restoration Ltd	11609 115TH ST
MSC	INTS0001	Interior Savings	9145 Main Street
MV	985.100	CANTRILL	9440 115TH ST
V	1315.000	Sunrise RV Sorage and Lofts - RV Storage	5803 Lakeshore
V	985.337	Fortis BC	10600 115TH ST
		Total # of Accounts	335
